



**FOURTH QUARTERLY
PROGRESS REPORT**
October - December 2008

**Community Based Approach
to Local Development Project**



Project is financed
by European Union



Project is cofinanced
and implemented by UNDP

TABLE OF CONTENTS

Executive Summary	4
I. Context	5-7
1.1 Project Genesis	6
1.3 Project Area	7
II. Project Activities and Results	8-28
2.1 Establishing Partnership with Regional Authorities	9
2.2 Establishing Partnership with Pilot Rayons	10
2.3 Establishing Partnership with Village/City Councils	12
2.4 Organising Local Communities	13
2.5 Developing Capacity	19
2.6 Community Projects	21
2.7 Communication and Visibility	24
2.8 Advisory and Management	26
III. Lessons And Opportunities	29-31
3.1 Stocking the Experience	30
3.2 Outlook for Future	31
IV. Annexure	32-61

LIST OF ABBREVIATIONS

ARC	Autonomous Republic of Crimea
CBA	Community Based Approach to Local Development Project
CIDP	Crimea Integration and Development Programme
CDA	Community Development Assistant
CDP	Community Development Plan
CRDP	Chernobyl Recovery and Development Programme
CO-MT	Community Organization Management Team
EC	European Commission
EU	European Union
LDF	Local Development Forum
MGSDP	Municipal Governance and Sustainable Development Programme
MoU	Memorandum of Understanding
MP	Micro Project
MPP	Micro Project Proposal
OC	Oblast Council
OCRC	Oblast Community Resource Centre (same as OIU)
OIU	Oblast Implementation Unit (same as OCRC)
OSA	Oblast State Administration
PA	Partnership Agreement
PMU	Project Management Unit
RC	Rayon Council
RSA	Rayon State Administration
UNDP	United Nations Development Programme

ACKNOWLEDGEMENT TO OUR PARTNERS

	Ministry of Regional Development and Construction		Secretariat of the Cabinet of Ministers of Ukraine		
	Cabinet of Ministers and Supreme Council of Autonomous Republic of Crimea		Cherkaska Oblast State Administration and Council		Chernihivska Oblast State Administration and Council
	Chernivetska Oblast State Administration and Council		Ivano-Frankivska Oblast State Administration and Council		Kharkivska Oblast State Administration and Council
	Khersonska Oblast State Administration and Council		Kirovohradska Oblast State Administration and Council		Khmelnytska Oblast State Administration and Council
	Kyivska Oblast State Administration and Council		Lvivska Oblast State Administration and Council		Mykolaivska Oblast State Administration and Council
	Poltavska Oblast State Administration and Council		Rivnenska Oblast State Administration and Council		Sumska Oblast State Administration and Council
	Vinnytska Oblast State Administration and Council		Volynska Oblast State Administration and Council		Ternopilska Oblast Administration and Council
	Zhytomyrska Oblast State Administration		Zakarpatska Oblast State Administration and Council		Zaporizka Oblast State Administration and Council

We acknowledge the support and cooperation on the part of the Government of Ukraine and our regional partners, namely Oblast State Administrations and Oblast Councils of Rivnenska, Poltavska, Sumska, Zhytomyrska, Ivano-Frankivska, Kirovohradska, Ternopilska, Lvivska, Vinnytska, Volynska, Chernivetska, Khmelnytska, Zakarpatska, Chernihivska, Khersonska, Kyivska, Luhanska, Zaporizka, Kharkivska, Mykolaivska, Cherkaska and oblasts and Autonomous Republic of Crimea. We also acknowledge the support of oblast authorities namely Oblast State Administrations and Councils of Dnipropetrovska, Odeska, Donetska and Luhanska oblasts for paving the way for partnership and launching of the Project in their oblasts during the first quarter.

Similarly, CBA team would like to thank all the institutions/individuals involved in the implementation process for their cooperation during the quarter, namely EC Delegation Office and UNDP management, Crimea Integration and Development Programme, Chornobyl Recovery and Development Programme, Municipal Governance and Sustainable Development Programme, officials of oblast and rayon state administrations/councils, NGOs, media, other public and private agencies.

Executive Summary

In the fourth quarter of 2008, implementation of CBA Project continued, with regional launching completed, and selection of pilot rayons and communities approaching almost to the end. Other important processes e.g. institutional development, capacity building, participatory planning, plan mainstreaming, implementation of community initiatives took place albeit at different scales. By end of 2008, all envisaged elements of CBA projects were put in place. Details about key activities are given hereunder:

Launching of Project in 3 regions took place during the quarter. It marked end of CBA launching in the regions. Similarly, 16 rayons were selected for partnership through competition in 2 regions. It marked completion of rayon selection in 24 regions. In total, 193 rayons were selected in all pilot oblasts, except Donetsk. Following to the rayon selection, 200 village/city councils were selected in 5 regions during the quarter. In total, selection of 964 village/city councils was completed by end of 2008.

In the reported period, focus of Project activities shifted towards actual community mobilization. Through community dialogues, 372 Community Organizations were formed in the IV quarter in participation of 39'778 community members. In total, number of COs formed during 2008 amounts to 701 with participation of 96'698 persons (60% female). To facilitate the process, CO-manual was prepared and disseminated.

262 training courses were held during the quarter to build capacity of community activists as well as focal persons from local governments. In cumulative term 299 trainings were held for 7497 persons (77% CO-members, 23% officials from local authorities) since inception.

475 COs prepared community development plans during the quarter. Of them, 355 plans were reviewed at Local Development Forum and 215 were approved by the Forum. Priority in the plans was focused on energy savings (48%, followed by health post (27%), water supply (18%), local transport (4%), environment (2%) and others (1%).

In the reported period, 47 communities' micro-project proposals were approved for funding. From CBA project side, financing was released for 12 micro-projects. Total cost of these projects was UAH 6.3 million of which 10% came from the beneficiary COs, 15% from the village/city councils, 34% from the rayon authorities, 2% from oblast authorities, 1% from the private sectors and remaining 39% from the CBA. A technical manual was prepared and disseminated to the COs and field offices to enhance the quality of work related with community initiatives.

With an aim to analyze progress of Project implementation and plan for 2009, joint review meeting and two cluster meetings were held during the 4th quarter in various regions. Similarly, one Steering Committee meeting and 2 donor/partner visits were held during the quarter to familiarise the CBA-stakeholders about the CBA activities.

Extensive media coverage of Project activities in the regions was traced. During the quarter, 235 media coverages were registered across Ukraine, including printed and electronic editions, radio and TV reportages. Total coverage during the year amounts to 780. Also, 32 issues of regional newsletters were published and disseminated among target audience.

In 2009, target will be accomplished in terms of partnership with the regions, rayons, VC/CCs and COs. Focus will be placed on capacity building, planning and implementation of community initiatives. It is aimed to initiate at least 850 community projects. Documentation and dissemination of lessons learned will be carried out vigorously.

Statistical Abstract

SN	Description	Description	Total Target	Achieved in Q4	Achieved since inception	%
1	Agreement with oblasts authorities and selection of pilot rayons	Regional seminars held	25	3	25	100.0
		PA signed with OSAs/OCs	24	2	20	83.3
		PA signed with ARC-Govt.	1	1	1	100.0
		Rayons selected	200	16	193	96.5
2	Training CBA Staff and national counterparts	Manual/guidelines prepared	3	2	3	100.0
		CBA staffs trained	59	15	74	100.0
		OSA-staffs trained	25	49	74	100.0
3	Information Campaign & Media Strategy	Communication strategy developed	1	1	1	100.0
		Visibility guidelines developed	-	-	1	100.0
		Media coverage (No.)	-	235	780	100.0
4	Selection of Target Communities	Rayon seminars held	200	16	193	96.5
		VC/CC selected	1000	200	964	96.4
5	Community mobilisation and training	COs formed	1000	375	701	70.1
		CO-members trained	-	n a	7497	100.0
		- COs registered	1000	228	351	35.1
6	CO planning & mainstreaming	CD Plan prepared	1175	475	595	50.6
		Plans discussed at LDFs	1175	355	375	31.9
		No. of projects approved	1175	40	47	4.0
		No. of micro-projects funded	1175	12	12	1.0

CHAPTER I



C O N T E X T

- 1.1 Project Genesis
- 1.2 Project Area

1.1 Project Genesis

1.1.1 Background

Ukraine has made significant economic development since its independence. However, it is still challenged by some serious issues. Economic growth is not equitable, with only small share of population benefiting from its fruit. Those who suffer most live in rural and semi-urban areas. Low living standards in these areas are characterized, besides low income, by insufficient access to medical care and education, underdeveloped (or worn out) basic infrastructure and poor access to drinking water. Social, health and environmental problems at local level have is very common and warrant serious attention.

These challenges form a part of the MDG signed by Ukraine in 2000. To achieve these goals, much work is needed, especially at local level. The experience around the world¹ indicate that solution to these challenges is contingent on empowerment and active involvement of local communities, and their capacity to identify development priorities and ensure their attainment. However, legacy of the highly centralised system of policy, planning, budgeting and decision-making is yet to be adequately geared towards accommodating the needs and priorities as perceived by citizens and local authorities. On the other hand, passive attitude of the population in general and limited capacity of the local governments in rural areas to generate revenue remains a challenge.

Experience of European Commission's projects on pilot models for sustainable regional and local development have indicated the need to emphasize 'bottom-up' approach in tackling social needs of the poor population. On the other hand, Area-Based Development (ABD) Approach promoted by UNDP Ukraine through its projects² has proven to be an effective way of achieving social goals in a decentralised manner. In close partnership with local authorities and local communities, ABD Approach unleashes the potential of the people to help themselves. It brings local authorities and communities together for joint problem-solving and development activities, thus reinforcing the MDGs.

Joint EC-UNDP initiative - the Community-Based Approach to Local Development (CBA) is founded on the achievements of ABD approach and is meant for applying its main tenets country-wide and provide valuable inputs for the ongoing policy debate on administrative and fiscal decentralisation and further democratisation of society. CBA Project was launched in September 2007 and functioning since January 2008.

1.1.2 Objectives

Main objective of the CBA Project is to create enabling environment for long-term self-sustaining social-economic and environmental development at local level throughout Ukraine.

Specific objectives of the Project are to:

- Improve living conditions in rural and (semi-) urban communities through sustainable community-based self-help initiatives;
- Demonstrate participatory local governance, joint decision making and public private partnership for decentralised public service delivery through self-governing community organisations;
- Enhance professional skills and knowledge of community organizations and local authorities to initiate and maintain participatory local process on sustainable social economic development and public services delivery;
- Document experience on participatory planning, decision-making and social action with a view to providing inputs for policy and legal reforms.

1.1.3 Project Strategy

The strategic goal of the CBA is to build capacity for participation of the local communities and local authorities into joint decision making process and use this capacity for multi-stakeholders cooperation and multi-sectoral interventions that are geared towards strengthening of local governance and sustainable

¹ As reflected in the conclusions of the World Summit (1992) at Rio de Jenerio and World Summit (2002) at Johannesburg. Local Agenda 21 (www.un.org/esa/sustdev/agenda21.htm) and Johannesburg Declaration (www.un.org/esa/sustdev/documents/Johannesburg%20Declaration.doc) may be browsed for details.

² Crimea Integration and Development Programme (CIDP); Chernobyl Recovery and Development Programme (CRDP); and Municipal Governance and Sustainable Development Programme (MGSDP)

human development with ensured local ownership of the process. To this end, following strategies are followed to materialise the objectives of the Programme.

All oblasts of Ukraine and in Autonomous Republic of Crimea form the overall project area of CBA while selected rayons, village/city councils and local communities form the functional area. Selection is based on the level of socio-economic hardship facing them. Partnership, based on willingness and commitment for cost sharing, form the basis of Project implementation in the selected area.

ABD approach is utilized to unleash the potentials of selected communities to address their common needs focused around health, environment, energy, water supply and local transportation. To this end, the selected communities are organised into 'community organisation (CO)' founded on norms of good governance.

Appropriate support structures are created at various levels to facilitate smooth implementation of the Project. Through networking of local communities, local/regional authorities, private sector and civil societies appropriate fora are established at rayon/oblast level so that they can hold regular dialogue on sustainable development envisioning, mainstreaming of community plans, deciding upon public-private partnership mechanism for implementation of local priorities and carrying out participatory monitoring. Networking of stakeholders at the national level enables overall monitoring and advisory support.

Capacity of duty-bearers in the local communities, local government as well as national level officials is complemented through capacity building activities. Capacity of the COs is built in such a way that they are able to make joint decision with local authorities, mobilize resources, implement local priorities and sustain the result. Capacity of the partners (VC/CC, rayon/oblast etc.) is strengthened in terms of human resources to implement participatory approach propagated by the Project. Training, exposure visits, dialogues and small grants (for community projects), appropriate institutional mechanisms etc. are used as tools for building capacity.

Appropriate management and information systems (MIS) is established to make the stakeholders directly involved in the process of monitoring and assessment of the Project activities. It includes process monitoring, input monitoring, output monitoring and impact monitoring. Flow of information is bottom-up and participatory.

Sustainability of the systems, institutions (community organizations etc.) and services established at local community level under support of the Project is ensured so as not to lose the principles and value propagated by the Project.


1.2 Project Area

CBA Project will work in all oblasts of Ukraine and Autonomous Republic of Crimea covering total of 200 rayons (eight in every oblast in average) and 1000 villages/settlements/cities (five in every rayon in average) with population less than 10.000 people.

CHAPTER II



PROJECT ACTIVITIES AND RESULTS

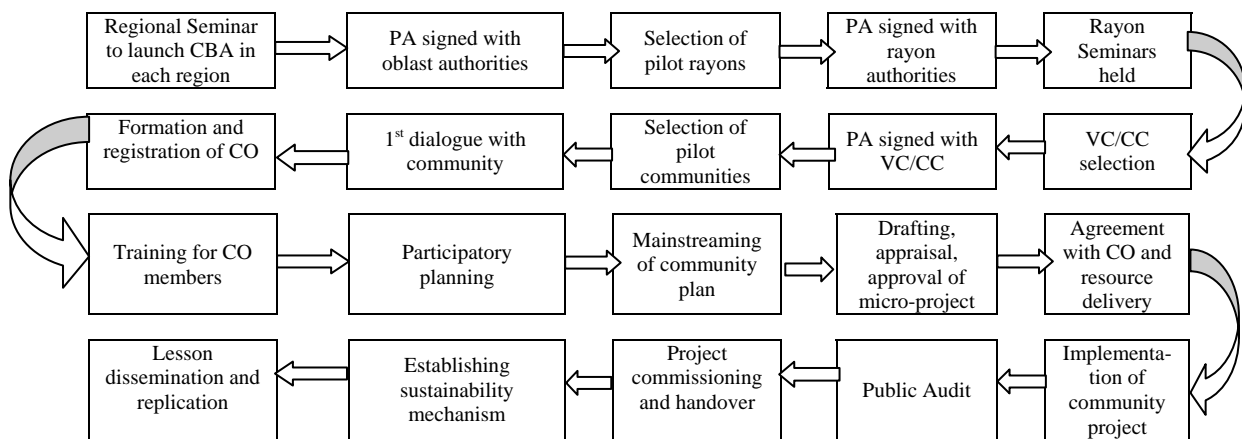

2.1 Establishment of Partnership with Regional Authorities

Establishment of formal partnership with oblast authorities, through signing of partnership agreement, is considered to be a milestone in CBA implementation. Such agreements are also essential to formalize the role and commitment of the partners (local authorities and UNDP) and to provide an official basis to work with community organizations. This activity includes two sub-activities described hereunder:

2.1.1 Holding regional meetings and regional seminars for presentation of CBA Project

In the reported period, 3 regional seminars were held to start project activities in Dnipropetrovska, Donetsk and Mykolaivska oblasts. Thus, project was launched in all regions of Ukraine in the presence of heads/deputy heads of oblast state administrations and oblast councils. Participants of the launching seminars included oblasts' and rayons' authorities including heads/deputy heads of OSAs, OCs, RSAs, RCs; representatives of NGOs and mass media and in some cases the heads/deputy heads of village/city councils.

2.1.2 Signing of partnership agreements with regional authorities

Signing of partnership agreement between UNDP and regional authorities is vital for effective implementation of the Project although it was not a pre-requisite for launching of the Project activities in the region. Often oblast authorities signed partnership agreement during the regional seminar, in presence of rayon authorities, NGOs and media. Where signing did not take place, regional seminars were held and call for rayons' participation was announced. In such cases, the oblast authorities signed partnership agreement at a later date.

During the quarter, 3 Partnership Agreements were signed, with ARC, Mykolaivska and Zaporizka oblasts. By December 2008, 21 partnership agreements were signed. Further details on establishment of partnerships with regional authorities are given in Annex - 1.

Odeska, Dnipropetrovska, Donetsk and Luhanska oblasts are currently reviewing partnership agreements.



2.2 Establishment of Partnership with Pilot Rayons

Establishment of formal partnership with rayon authorities, through signing of partnership agreement, is considered to be second milestone in CBA implementation. It ensures clear role and commitment of the rayon authorities and provides an official basis to reach village/city councils. To this end, following steps were followed during the quarter.

2.2.1 Selection of pilot rayons

As a primary step, announcement was made in the last 3 oblasts during each regional seminar for rayon authorities to send application forms to CBA office within 3 weeks. This announcement was for ensuring the principle of competition and transparency. In total, such announcements were made in 25 Seminars since beginning of 2008.

As a follow up action to the announcement, the interested rayon authorities sent their application to the CBA office. The applications included information on social/economic/environmental hardship (access to water supply, access to medical services, environment situation, energy saving, school transportation) facing the rayon and level of commitment expressed by the rayon authority. Received rayon applications were reviewed and analyzed by CBA Project in light of the information received from the rayon and oblast authorities and rayons of each oblast were ranked according to the hardship facing them. In the reported period, 20 applications were received from rayons of Cherkaska oblast and 9 applications from rayons of Dnipropetrovska oblast. Call for participation was announced for rayons of Donetsk oblast on 18 December.

Selection of the pilot rayons for each region was done by a 'Rayon Selection Committee' consisting of representatives from the respective oblast state administration and oblast council, UNDP and CBA Project. During the quarter, meetings of then Rayon Selection Committees were held for 2 oblasts: Mykolaivska and Dnipropetrovska. See Annex - 2 for summary of the meetings and the list of selected rayons.

Cumulatively, 193 rayons of 24 regions (except Donetsk oblast) are involved in cooperation with CBA Project.

2.2.2 Holding rayon seminars

Rayon selection was followed by rayon level seminars in each oblast to sensitize rayon officials and officials of village/city councils and make announcement for village/city council application.

During the quarter, 16 rayon seminars were held in Mykolaivska and Dnipropetrovska oblasts. Since inception, 193 rayon seminars were held in 24 regions (except Donetsk oblast). In total, 5966 officials, including heads of RSAs and RCs; heads of village/city councils; heads of relevant departments of RSAs and RCs and 263 media representatives attended the events.

In the seminars, focus was placed on importance of participatory approach; introducing the CBA Project and its modus operandi, highlighting experiences of EU Tacis and UNDP-projects on participatory approach. To sensitize the audience further, the film, "A Step Ahead: How Ukrainian Communities Are Helping Themselves" was shown featuring success stories of UNDP projects namely CRDP, CIDP and MGSDP. These information were followed by discussion on terms of partnership with rayon authorities and village/city councils, call for application from the village/city councils for partnership with the Project and criteria of village/city council selection.

Officials of the OSAs and OCs were key speakers during the seminars along with the CDAs and CDS of PMU, who presented the CBA project to the participants. Ownership shown by the oblast authorities in reaching rayons is expected to have strong positive effect on the result of the Project (Table - I, Annex - 3 for summary of participation of local counterparts in rayon seminars). Participation of CDS was mainly limited to initial backstopping, upon which the CDAs and oblast teams were able to continue with rayon seminars on their own.

Table – I: Participation of Officials in the Rayon Seminar

SN	Oblast	Seminar held	Total No of participants	No of media	Participation of officials in the rayon seminar by no. of event				
					OSA*	OC*	OSA-FP	CBA-CDS	CBA-CDO
1	Dnipropetrovska	8	198	9	2	0	2	2	8
2	Cherkaska	8	274	17	1	0	1	1	8
	Total	16	472	26	3	0	3	3	16
	Cumulative	193	5966	263	15	19	52	42	194

OSA* = top-level official of OSA; OC* = top level official of OC; OSA-FP = OSA focal point;
CBA-CDS = CBA community development specialist; CBA-CDO = CBA community development officer;

2.2.3 Signing partnership agreement between UNDP and rayon authorities

Of the 193 rayons involved in CBA activities, 177 Partnership Agreements with rayon authorities were signed in course of the seminar or at a later date. Of them, 20 were signed in the fourth quarter, in Poltavsla, Kharkivska and Mykolaivska oblasts.

In general, both authorities namely the rayon council and the rayon state administration signed the Agreements indicating their full support to the Project activities. In some cases, signing of Agreement took longer time because the responsible authorities were not available or the responsible legal department took time to review the document. Also, some rayon authorities waited for oblast authorities to sign Agreement first.



Photo - 1. Establishing partnership with Koropskyi rayon, Chernihivska oblast

2.2.4 Project Coordination at Rayon Level

In the framewok of partnership, practical cooperation with rayon authorities continues primarily through the mechanism of holding joint Local Development Forums (LDF). These forums are established by a decree of local administration, in each partner rayon, as per the provision in the partnership with RSA/RC. Typical structure of LDF is given in Box 1. LDF aims to facilitate dialogue, coordination, planning and decision-making at local level between the oblast and rayon authorities and communities for promoting integration and development. Meetings are held once in 2-3 months to discuss local development issues and mainstream community plans. LDFs' specific task regarding CBA implementation is to support community organizations for technical backstopping and resource mobilization implementation and handover of community projects.



Photo - 2. Local Development Forum in Pidvolochysk, Lvivska oblast

During the quarter, LDFs were formed in 75 rayons, and 79 sittings were held. Since inception, 100 Forums held 104 meetings.

Box - 1 Typical structure of a LDF

- Head of the Rayon State Administration (Chairperson)
- Chairman of the Rayon Council (Member)
- Heads of the village/city councils covered by CBA (Member)
- Chief of line units (including 5 CBA areas) in RSA (Member)
- Representatives of oblast authorities (Member)
- Chairpersons of COs formed by CBA (Member)

As ad-hoc members, representative of Commercial Banks, local NGOs, public utility companies and other organizations can be invited if and when required.

Box - 2

Practice of holding LDFs beyond CBA pilot rayons

In Ivano-Frankivska oblast, management of OSA was impressed by the efficiency of Local Development Forums, so idea was generated and supported to similar forums in other rayons, including those which do not participate in CBA Project. These regular meetings will be called Local Economic Forums, a wider range of economic problems will be discussed there organized by oblast/rayon leadership and will as a wider range of problems will be discussed there.

2.3 Establishing Partnership with Village/City Councils

During the reported period, 466 applications for partnership were received from village/city councils of 5 regions namely Mykolaivska, Kirovohradska, Kharkivska, Dnipropetrovska and Cherkaska.

The team of the oblast community resource centre analysed the information of the applications and information received from the respective rayon state administrations. Based on the analysis, they made a ranking of the participating local councils based on the socio-economic hardship and commitment. The analysis and ranking was further reviewed by related specialists of the PMU.

The ranked applicants were discussed in 'village/city council selection committee' meetings held for the rayons ready for VC/CC selection. In the 4th quarter, 200 local councils were selected from 5 regions for CBA Project as shown in Table - II, Annexes - 4 and 5. In all cases, the meeting was presided by CBA focal point of Oblast State Administration. Other participants of the meeting included representatives from regional council, rayon state administrations, rayon councils, and CDAs in the oblast. Local partners' feedback and opinions are quoted in Box 3.

Total number of pilot local councils amounts to 964, of them 830 are village councils, 114 town councils and 20 city councils.

Table – II : Selection of Village/City Councils

№	Name of Rayon	No of Rayons	No of applications	No of selected local councils			No of local councils in reserve		
				VC	TC	CC	VC	TC	CC
1	Cherkaska	8	117	39	0	1	23	0	0
2	Dnipropetrovska	8	54	38	2	0	11	3	0
3	Kharkivska	8	111	38	2	0	56	1	0
4	Kirovohradska	8	105	37	3	0	22	2	0
5	Mykolaivska	8	79	35	5	0	40	0	0
	Total	40	466	187	12	1	112	6	0
	Cumulative	193	2478	830	114	20	541	18	2

VC - village council (сільська рада), TC - town council (селищна рада), CC - city council (міська рада)

In the 4th quarter, official terms of partnership were signed with 269 village/city councils, total amount of partnerships since inception is 440, as given in Table -III.

Table – III: Summary of Establishment of Partnerships with VC/CC in 2008

	Oblast	PA in Q-4	PA in 2008	№	Oblast	PA in Q-4	PA in 2008
1	ARC	7	11	14	Lvivska	10	37
2	Cherkaska	0	0	15	Mykolaivska	0	0
3	Chernihivska	6	6	16	Odeska	0	0
3	Chernivetska	0	20	17	Poltavska	24	24
5	Dnipropetrovska	0	0	18	Rivnenska	27	27
6	Donetska	0	0	19	Sumska	0	0
7	Ivano-Frankivska	10	35	20	Ternopil'ska	20	20
8	Kharkivska	35	35	21	Vinnyska	0	11
9	Khersonska	17	40	22	Volynska	37	37
10	Khmelnyska	0	21	23	Zakarpatska	10	10
11	Kirovohradska	25	25	24	Zaporizka	0	0
12	Kyivska	41	41	25	Zhytomyrska	0	0
13	Luhanska	0	40		TOTAL	269	440

Box - 3**Opinions of Local Partners about CBA Project**

- *Implementation of CBA Project will become a great school of professional skills for our bodies of self-organisation.* (Mykola Gruby, Deputy Head of Perechynska RC, Zakarpatska oblast)
- *It's a very positive process that will allow us to find an understanding between authorities and community.* (Grygoriy Targonskyi, Deputy Head of Rokytnivska RSA, Rivnenska oblast)
- *Administrative-territorial reform is an inevitable future. After its implementation, the leading role will belong to local communities, so we need to start preparing people for this already now.* (Leonid Orlov, Head of Novomyrhorodskyi Rayon Council, Kirovohradska oblast)
- *How many things we did not know before! We could have used it long ago to improve our community's life!* (Ganna Zelinska, Deputy Head of Zariyvka village, Khersonska oblast)
- *It's worth creating communities not only for implementation of this specific project, but for the perspectives of realization of other initiatives that may come up in the future. For this, real activists should be elected to guide the community.* (M. Katrych, head of Golovetska VC, Starosambirskyi rayon, Lvivska oblast)
- *Since Mostytskyi rayon is a border region, the high quality training of communities will help to prepare them to participate in other EU projects, where organizational and managerial requirements are very high.* (V. Klochkov, CBA Project coordinator in Mostytsky rayon, Lvivska oblast)
- *It's high time for communities to take responsibility for their settlement's development!* (Valentyna Chumak – Head of the HR Department of Slavutskyi RSA, Khmelnytska oblast)
- *Development and empowerment of local communities, their active involvement in solving their own problems is very important for Sokyrianskyi rayon, as it will allow to manage more efficiently its resources. Participating in socillay important activities, community members are likely to feel real patriots of their «little homeland».* (Vasyl Kozak, Head of Sokyrianskyi Rayon Council, Chernivetska oblast)
- *Preliminary planning of the village development is very important for community organisation, as it will help to set the list of problems, priorities and tasks to be accomplished within a certain period of time.* (Victor Yavetskyi, Deputy Head of Hertsavskyi Rayon Council, Chernivetska oblast)
- *Peopledont' believe in themselves and have no trust to their leaders because for a long period of time situation in villages was only getting worse, and no real work was done. We hope the participation in teh CBA Project will change this situation.* (V. Umanets, deputy Head of RSA, Chernihivska oblast)
- *We strive to seel the first results of the Project, to receive the financing, accomplish the task and demonstrate this experience to other communities of the region* (V. Chernukha, Acting Head of Koryukivska RSA, Chernihivska oblast)
- *Participatory planing is an interesting methodology, but how to use it in practice ? (...) I think we should find a common problem concerning everyone. It should become the priority. For us it is a water supply system.* (Head of Drozdivskyi Village Council of Kulykivskyi rayon, Chernihivska oblast)
- *If we want to organise an active community, we must involve it into the work planning. Participatory planning helps to develop a strategy, set priorities, sort out tasks. Finally, this method allows to involve the villagers in decision making an the first stage of our work with communities.* (Tetyana Danylova, Head of regional Development Department, Chernihivska OSA)
- *Thanks to participation in the project, the rayon will have another unique chance to improve living conditions in the village communities.* (Oleh Nagyriak, Head of Chesnyky village, Rogatynskyi rayon, Ivano-Frankivska oblast)

2.4 Organising Local Communities

Following to selection of village/city councils, steps were taken to select the settlement(s) / local community and mobilize them for concrete action under the framework of CBA Project. By the end of December 2008, 794 local communities were organised to work with CBA through following process:

2.4.1 Holding VC/CC level seminar

Orientation was organised in the selected VCs/CCs, individually or collectively, to present CBA Project to the council members, VC/CC-executives, active citizens, NGOs and businesses from the locality.



Photo - 3. Village Council Seminars in Dyman Druhyi of Reshetylivskiy rayon, Poltavaska oblast

In perspective of the partnership with oblast and rayon authorities, the seminar focused on sensitizing the local representatives with importance of community-based approach to local development and explaining them the relevant procedure and conditions to achieve concrete results. Participation of the oblast and rayon officials in these local seminars reflected their commitment towards citizens' participation in decision-making process and raised effectiveness of the seminar (Table - IV).

In the 4th quarter, 530 VC/CC level seminars were held in 21 regions. During the 1st year of project activities, 897 seminars were conducted in all regions except Donetsk oblast.

Table - IV: Participation of Regional Officials in the VC/CC Seminar

SN	Oblast	No of seminars	No of participants	Participants		
				OSA FP	RSA FP	Leadership/employee of RSA/RC
1	ARC	11	181	0	11	16
2	Cherkaska	25	338	0	10	10
3	Chernihivska	40	1012	8	24	71
4	Chernivetska	40	970	5	15	25
5	Dnipropetrovska	18	441	0	0	16
6	Ivano-Frankivska	15	474	0	20	20
7	Kharkivska	40	721	5	12	32
8	Khersonska	15	610	0	15	19
9	Khmelnyska	40	1280	1	20	45
10	Kirovohradska	25	1121	0	25	40
11	Kyivska	17	700	0	13	12
12	Lvivska	10	149	10	10	10
13	Mykolaivska	40	1187	0	33	33
14	Odeska	25	380	5	24	5
15	Poltavska	16	376	0	2	10
16	Sumska	22	437	0	22	21
17	Ternopil'ska	11	198	0	10	3
18	Vinnyska	10	304	9	0	9
19	Volynska	40	711	40	40	63
20	Zakarpatska	30	760	0	26	6
21	Zaporizka	40	1233	0	40	48
	Total	530	13583	83	372	514
	Cumulative	897	14799	62	478	486

OSA-FP = OSA focal point; RSA-FP = PSA Focal Point;

Box - 4. Ownership of the Project as Demonstrated by Local Authorities

Outstanding enthusiasm and ownership of the Project was demonstrated by leadership of Snihurivskiy Rayon (Mykolaiivska oblast) where Head of RC, Mr. Valeriy Kozyrev, participated in every village council seminar and all the first meetings with communities, motivating and encouraging communities to actively participate in the Project.

“Yet 1,5 years ago I would not believe that such an approach works”, says Mr.Kozyrev, “But now I am confident of it and I want to share this confidence with our people. We have the example when gasification of the village was done by a self-organized community, while there is still no gas supply in the rayon capital. We followed the example of Voznesensk city, which participated in MGSDP programme, and saw that the approach really works. Recently, Snihurivka presented 3 projects for the competition for small/medium grants, and won financing for all of them.”

2.4.2 Selection of local community for partnership

Subsequent to the VC/CC seminar, the participants discussed on the comparative situation of the settlements belonging to the council from the perspective of socio-economic hardship facing them e.g. water supply, health services, energy efficiency, environment and school transportation etc. Based on the ranking, one settlement was selected for CBA Project. Alternative arrangement was necessary to ensure competition and attract the community which was the most willing and committed to apply self-help approach to resolve their problem.

During the quarter, 413 communities were selected for partnership. Cumulatively, the number of pilot communities is 794, with 276 communities in reserve list. See Annex - 6 for details on selection of local communities.

2.4.3 Formation of Community Organisation (CO)

Pursuant to the community selection, dialogues were held with the selected communities to sensitize them about importance of collective effort to resolve local development issues in partnership with local authorities and other development agencies including CBA Project (Box - 5) . Summary of dialogues per oblast is given in Table - V.



Photo - 3: First dialogue with community, Ternopil'ska oblast



Photo - 4: Community voting for participation in CBA, first dialogue in Honcharivka village, Odeska oblast

Box - 5. Holding Dialogues with Communities

Helping communities to get self-organized, Community Development Officers have to hold regular dialogues with them. In the CBA Project, at least 4 dialogues are foreseen:

Dialogue – I: To familiarise the inhabitants regarding importance of 'organisation, capital and skill' and process of forming community organisation (CO) based on the elements of good governance;

Dialogue – II: To familiarise the CO-members with the need and process of participatory planning and bottom-up planning process;

Dialogue – III: To familiarize the CO-members with the process of establishing accountability, transparency and participatory monitoring;

Dialogue – IV: To familiarize the CO-members with the concept and process of sustainability of services and benefits

Box - 6. Local Authorities participate in trainings for COs to share experience

In Kharkiv'ska oblast, for dialogues with communities oblast, CDOs invited representatives of RSA/RC who recently went through related trainings abroad (in Poland, Lithuania etc).

They provide the audience with real-life examples of communities' pro-active attitude and achievements of Community Organizations.

As a result, communities got inspired, furthermore they got more confidence as they received confirmation from authorities that the community based approach works and will be supported by local government.

Table - V. Dialogues with COs in 2008

Oblast	1st dialogue		2nd dialogue		3rd dialogue	
	Q-4	Total 2008	Q-4	Total 2008	Q-4	Total 2008
ARC	11	35	10	32	7	7
Cherkaska	0	0	0	0	0	0
Chernihivska	4	40	12	21	7	7
Chernivetska	10	40	0	0	0	0
Dnipropetrovska	1	1	0	0	0	0
Donetska	0	0	0	0	0	0
I-Frankivska	15	40	15	15	2	2
Kharkivska	20	20	0	0	0	0
Khersonska	40	40	0	0	0	0
Khmelnyska	10	39	20	20	0	0
Kirovohradska	25	25	0	0	0	0
Kyivska	43	50	44	44	3	3
Luhanska	0	40	0	40	3	3
Lvivska	10	40	3	3	3	3
Mykolaivska	40	40	13	13	0	0
Odeska	17	17	0	0	0	0
Poltavska	29	44	0	0	0	0
Rivnenska	1	40	35	40	0	0
Sumska	28	28	20	20	0	0
Ternopil'ska	2	42	28	28	0	0
Vinnytska	15	25	0	11	10	10
Volynska	30	37	25	25	0	0
Zakarpatska	40	40	0	0	0	0
Zaporizka	2	43	0	0	0	0
Zhytomyrska	20	40	0	39	0	0
TOTAL	413	806	225	351	35	35

**Photo - 5.** CO members, Petrovka village, Odeska oblast during 2nd dialogue**Photo - 6.** Community of Hrushiv village, Kyivska oblast at the 1st dialogue

As a result of the dialogues, in the IV quarter 372 COs were formed by 39'778 community member, of them 35% are males and 65% are females. (see Table - VI). Since inception, 701 CO were formed. Details of CO formation in the overall period of Project implementation are given in Annex - 7.

Table - VI: Formation of Community Organisation in IV quarter

№	Oblast	No of rayons involved	No of VC/CC involved	No of COs			No of h/h in village	Participating H/H		CO members		
				Formed	Enrolled with VC/CC	Legally registered		No	In %	M	F	Total
1	ARC	8	35	35	32	29	12293	9640	78%	12467	16459	28926
2	Chernivetska	0	0	0	0	0	0	0	0	0	0	0
3	I-Frankivska	8	40	26	23	2	4893	3327	68%	1969	2950	4919
4	Kharkivska	8	40	18	18	5	9576	8312	87%	4007	8461	12813
5	Kirovohradska	0	0	0	0	0	0	0	0	0	0	0
6	Kyivska	0	0	0	0	0	0	0	0	0	0	0
7	Luhanska	3	15	15	10	10	748	599	48%	174	300	474
8	Lvivska	3	15	15	7	5	9576	8312	14%	4007	8461	12813
9	Mykolaivska	8	8	20	20	20	15153	2429	42%	1421	2027	3448
10	Odeska	8	40	39	12	7	13630	3533	13%	559	1232	1801
11	Poltavska	5	25	20	10	10	8099	1805	16%	605	1406	2011
12	Sumska	9	41	43	43	38	32157	3183	39%	1310	1873	3183
13	Ternopil'ska	8	32	32	14	11	5288	2537	75%	2567	4048	6615
14	Vinnytska	8	37	37	5	5	11292	1583	79%	600	983	1583
15	Volynska	8	40	29	0	10	12968	1069	8%	561	1060	1 621
16	Zakarpatska	8	16	15	9	5	7017	4912	70%	2011	2901	4912
17	Zaporizka	8	40	33	33	8	19657	3089	23%	1205	1884	3089
	Total	103	409	372	295	228	99117	31382		13966	23532	39778
	Cumulative	162	731	701	473	351	267876	82122		38254	58089	96698

Box - 7. Pro-Active Attitude Makes Difference

In Luhanska oblast, outstanding activation of rural communities was observed even before any mobilization activities were carried out by CBA staff, e.g., before training was conducted for activists of Mistky village (Svativskyi rayon) and Kalmykivka village (Starobilskyi rayon), they initiated meetings with their communities, created and registered COs as legal entities, and elaborated first drafts of micro-project proposals. To receive all the necessary information, they were regularly contacting rayon focal points and CBA CRC. Such a proactive approach allowed them to surpass many other communities that already received training but are still not ready with their project proposals.

In generic sense, an organisation created by the citizens of a local community to address their common needs is considered as a community organisation (CO) or a community-based organisation (CBO). In legal term a CO or CBO can take different legal form as defined by the law of Ukraine e.g. association of co-owners of multi-storey building, housing committee, bodies of self-organisation of population, cooperative, public organisation, civil society organisation etc.

Of 384 legally registered Community Organizations formed within the framework of CBA Project, 12 are association of co-owners of multi-storey building; 13 cooperatives; 44 bodies of self-organisation of population; 305 public/civil society organizations and 6 charity organizations (see Table - VII for details).

Table - VII. Legal Form of COs

№	Oblast	No of COs			Legal forms of COs				
		Formed	Enrolled with VC/CC	Legally registered	ACMB	Cooperatives	BSP	PO	Others
1	ARC	35	32	29	0	4	25	0	0
2	Cherkaska	0	0	0	0	0	0	0	0
3	Chernihivska	26	23	2	0	0	1	1	0
4	Chernivetska	18	18	5	0	0	0	5	0
5	Dnipropetrovska	0	0	0	0	0	0	0	0
6	Donetska	0	0	0	0	0	0	0	0
7	I-Frankivska	40	35	35	0	0	0	35	0
8	Kharkivska	15	7	5	0	0	0	5	0
9	Khersonska	40	40	25	1	0	0	24	0
10	Khmelnyska	39	12	10	0	0	0	6	0
11	Kirovohradska	20	10	10	0	0	0	10	0
12	Kyivska	43	43	38	1	2	0	30	5
13	Luhanska	32	14	11	0	0	0	11	0
14	Lvivska	37	5	5	0	0	0	4	1
15	Mykolaivska	29	0	10	1	2	0	7	0
16	Odeska	15	9	5	3	1	1	0	0
17	Poltavska	33	33	8	0	2	0	6	0
18	Rivnenska	47	44	44	5	0	0	39	0
19	Sumska	28	20	16	0	0	0	16	0
20	Ternopil'ska	41	33	31	0	0	6	25	0
21	Vinnyska	11	10	10	0	1	0	9	0
22	Volyn'ska	37	27	27	0	0	11	16	0
23	Zakarpatska	37	29	15	0	1	0	14	0
24	Zaporizka	39	35	23	0	0	0	23	0
25	Zhytomyrska	39	38	20	1	0	0	19	0
	Total	701	517	384	12	13	44	305	6

ACMB - association of co-owners of multi-storey building; BSP - bodies of self-organisation of population; PO - public/civil society organizations

2.4.4 Organizational Maturity

It is important that the CO must reach certain level of maturity before undertaking development task of significant size. To this end, for about 1-2 months the CO should undertake small social/economic/environmental activities of household and community nature within its own capacity and from the resources available locally.

Most CBA communities implements self-funded initiatives before they receive funding for their micro-project. Typical cases of such initiatives are: related repair works, cleaning the nearby territory, planting trees etc.

Box - 8. Indicators of CO Maturity

CO-meeting is held regularly and in participation of minimum of 80% members
 System of making consensus based decision is established
 Accounts are kept transparently and in auditable form
 Concept of accountability is known to all
 Equity and inclusion criteria is built in the activities initiated/carried out by the CO
 It collects financial resources necessary for its development and its members pay commitment dues on regular basis
 It is enrolled with the village/city council (if it is not a BSP)
 It has carried out at least one development activity with visible result
 It has maintained management information system
 All decisions on key matters are taken by the general members whereas decisions on day to day management are taken by the executive body
 A financial ceiling has been set to cover most of the decisions on expenditures related with day to day management indicating that beyond this ceiling the decision will be made through general members
 All meetings, sessions and decisions made are drawn up by corresponding protocols
 The CO-members are willing to be accountable for all the decisions made by them and are willing to hold CO-MT accountable for any wrong doing
 The management of the CO acts on the behalf of its members and reports to them about the activities it performs
 CO follows the principles of gender equality
 The executive body constantly communicates with the bodies of local authority and other development agencies
 Must have tried participatory assessment of the CO, at least once

Box - 9. Organized Communities Can Do Much More

Before communities receive funding from CBA Project, they go participate in a series of orientation meetings, dialogues and trainings. Through these activities, communities realize their capacities and, in parallel to preparation of CBA micro-project, they start performing activities aimed at improvement of their living conditions. Below, are a few such cases.

☀ Case I. Volynska oblast

Community of Sedlyshe village (of Liubeshivskiy rayon) was the most active to get self-organized, defined the list of problems and priorities and created a CO "Femida". After participation in trainings, CO "Femida" was the first to draft project proposal and had it approved by Local Development Forum. Community members already gathered their part of the share for co-financing.

Waiting for the final approval of their micro-project, community does not waste time. They hold regular meetings to decide how to solve other problems: (a) community is now dealing with improving sanitation in local school, (b) community has initiated the process of allocation of additional premises or building an extension to arrange a VC there, (c) problem of hot water supply is also being solved.

☀ Case II. Ternopilska oblast

Awaiting for CBA funding for their micro-projects, the Community Organization "Oberih" (Hnylytsi village of Pidvolochyskiy rayon) started implementing self-funded initiatives, such as repair of the road, plantation of trees in local park and repair of memorial. For this, they used the money collected as membership fees. Also, CO managed to mobilize around UAH 28.000 of local sponsor's funds.

Other examples of such local initiatives in Ternopilska oblast include installation of street lighting system (Bilokrynytsia village of Zborivskiy rayon), repairing roads (village of Horishnya Slobidka, Monastyrskiy rayon), installation of water supply system in local school (Tseliiv village of Husyatynskiy rayon).

☀ Case III. Khersonska oblast

Daryivska village council was the first to express its interest in CBA Project. Within this village council, 3 community organizations were created and registered. Each of them competed for participation in CBA. They had their priorities defined and collected money for co-financing of micro-projects. Dilemma was solved when 3 communities jointly decided that the CO №1 with micro-project on repair of the roof of kindergarten should be given priority.

CO №2 decided to implement their project on reconstruction of transformer vault independently, using UAH 18'000 of collected community money. As a result of their activation, they also received additional funding from rayon budget (UAH 80'000). CO №3 also started with self-funded initiatives on repair works in their multi-apartment building, using funds collected from inhabitants (UAH 16'000), and is looking for additional donor/sponsor funds.

2.5 Developing Capacity

Capacity building is one of the crucial activities of CBA Project. It involves such activities as training, exposure visits, dialogues and various other forms of techniques utilized for skill enhancement/knowledge transfer. The purpose is to enable local communities, local authorities and other partners to adopt and practice the approach promoted by the Project. During the quarter, 2 capacity building events took place. Details on these events are given hereunder:

2.5.1 Training of CBA project staff and national counterparts

During the quarter, 2 training courses were organized for CDAs and rayon focal points in the form of cluster meetings.

- Cluster 1: ARC, Mykolaiivska, Odeska and Khersonska oblasti.
- Cluster 2: Ivano-Frankivska, Lvivska, Zakarpatska, Ternopilka and Chernivetska oblasti.

First cluster met in Yevpatoria, ARC on 19-20 November, second cluster gathered in Ivano-Frankivsk on 24-25 November. Goal of the cluster meetings was twofold: (a) to review progress of each OIU and make plans for 2009; (b) to train rayon focal points on the mechanisms of community based approach and prepare them for their role of coordinators of rayon Community Resource Centres.



Photo - 7. Cluster meeting in Ivano-Frankivsk



Photo - 8. Cluster meeting in Yevpatoria

A total of 64 persons benefited from the training namely 15 Project staffs and 49 officials of counterpart agencies (oblast state administrations).

As follows from analysis of evaluation forms, most participants were entirely satisfied with training and considered it highly interesting. Length of the training was mostly estimated as optimal, a less numerous group (25%) wished it was longer. 83% estimated the level of trainer as excellent and characterized training techniques and methods as most appropriate and efficient. 71% of participant noted that the training considerably helped them to improve their knowledge on the subject (see Annexes - 9A and 9B for details). Participants' feedback on cluster trainings is quoted in Box - 10.

Box - 10. Opinion of Training Participants

- *At the training, I acquired a lot of new knowledge and experience and got fuelled with energy that I will now share with communities of my rayon. Training was very well organized, I very much hope that our cooperation will continue in future and bring positive results.* (I.Khymych, Savranskyi rayon)
- *We learned a lot of new interesting and useful things, the training certainly enriched our experience. It was especially impressive to learn about experience of Crimean communities: of Saky city and Krymske village.* (O.Bahuzova, Kotovskyi rayon)
- *After the training, all the doubts I had about possibility to realize projects in rural area are gone. They are replaced with certitude that we are going to achieve positive result. Knowledge we gained at the training will enable me to act more efficiently so that our initiative is implemented as soon as possible. I will also feel much more confident when explaining community-based approach to the people.* (E.Zhyeva, Head of Zhovtneve village council)

2.5.2 Training for Community Organizations

The success of an organisation largely depends on (a) capacity of its executive body to manage the organisation and its activities (b) knowledge and understanding of its general members about the principles of sustainable development and good governance. Therefore, the regional teams of CBA implementation units organize trainings for CO-MT and counterparts/focal points of corresponding local councils which allows for a higher degree of involvement and engagement of local counterparts.

CBA Project offers training and orientation courses for CO-members in following areas –

- 1) CO Management and planning;
- 2) Book-keeping in CO;
- 3) Community planning;
- 4) Drafting MPP.



Photo - 9. Training in Ochakivska village, Mykolaivska oblast

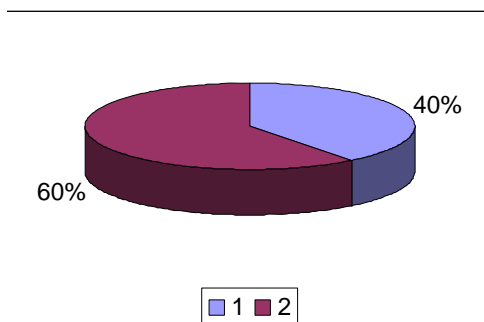


Photo - 11. Training in Antoniny, Khmelnytska oblast

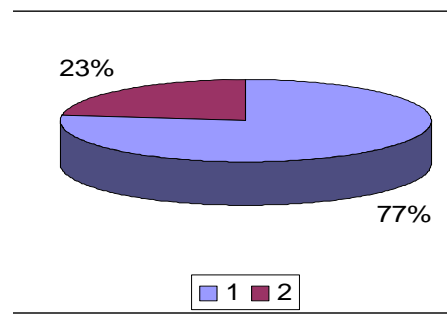


Photo - 10. Training in Pereyaslav, Kyivska oblast

In the reported period, 262 trainings were held, cumulatively since inception - 299 trainings. Through these, 7497 persons (of them, 40% males and 60% females) were faminiarized with the essence of community-based approach, learned how to create, register and maintain Community organization, how to write and defend a project proposal, and how to implement an initiative on improvelment of living quality of local community. 23% of participants were representatives of local authorities, i.e. focal points from village/city councils. Statistics of participation in trainings for COs is given in Diagram - 1, participants' feedback is analyzed in Annex - 8.



1. males
2. females



1. members of COs
2. representatives of local authorities

Box - 11. Opinion of CO Members on trainings

- *The rayon authorities believe that our village has no perspectives, but we will struggle to change this opinion.* (Stanislav Metelsky – CO leader Puzyrky village, Ivanivsky VC, Slavutsky rayon, Khmelnytska oblast)
- *Training on «effective planning» can be characterised like Stefanyk's short stories : brief, strong and dramatic.. Nice and clear, comprehensible performance. Optimistic.* (Galyna Serdyuk, CO memembr, Zuhkotyn village, Kolomyyskiy rayon, Ivano-Frankivska oblast)
- *We expect that the Project will help to unite our community, because politicians only divide it.* (Lidiya Rozhok, Leader of the Community of Sulzhyn village, Shepetivskiy rayon, Khmelnytska oblast)
- *After training, I understood how much of the strength a community possesses; it is a real force that will overcome all the hardships.* (Victor Mushyn, School Headmaster, Head of «Beregynia» charity fund, Mykolaivska oblast)
- *I understood, that a united community can move mountains. It turns out that everything is possible, and all we have to do is to join our efforts. It will be a crime if we miss this chance.* (Victor Klymets, Activist of CO «Svitanok», Samenskiy rayon, Rivnenska oblast)
- *It's an extremely interesting approach, the one proposed by the CBA Project. If people care about their own lives, they should unite and stop looking who to blame for their misfortunes. We are primarily thankful for incentive to develop that we received from the Project.* (Olga Yuschuk, Head of CO «Leleka», Rivnenska oblast)
- *We are grateful for the training, thanks to which we've discovered the perspectives we will have as a legal entity (NGO) and what challenges we can expect. At trainings for communities from 5 villages we exchanged experience, shared some good examples of solving local problems, discussed common problems. Such trainings inspire to joint work for public benefit.* (Oleksandr Yaskovets, secretary of Koretska CO «Nadiya», Rivnenska oblast)
- *Thanks to this training for the first time I realised the role of planning and how important it is to apply a complex strategic approach to solve community problems. I also realized why each villager has to participate in the creation of a joint plan.* (Tetyana Dubych, functional group member Babynska CO « Promin », Rivnenska oblast)
- *Common trainings are also an opportunity to learn about problems in neighbouring communities of the rayon and exchange experience of solving them. We realize that the result will entirely depend on our work. However hard it may be, we'll go till the end.* (Olena Susidska, Head of CO of Bakyrivka village, Okhtyrsky rayon, Sumaska oblast)
- *Planning of CO activities is the first real step towards creation of a strong community.* (V. Vudmaska, Head of CO of Stuzhytsya village, Zakarpatska oblast)
- *The training allowed me to understand what opportunities our village has, I also realized we don't need to wait for the time when our local budget will be big enough to allocate us some money.* (CO "Window to Europe" Velykoburlutskiy rayon, Kharkivska oblast)
- *Everything was clear and interesting. Community organisation does not seem now such a «scary» thing. We are eager to act.* (Community activist Zarichya village of Volodymyro-Volynsky rayon, Volynska oblast)
- *I always believed, that only males can solve serious problems. Thanks to the training, now I am not afraid to try myself to help to set street lighting in our village.* (Community activist Verkhniv village Buzhankivska VC Ivanychivsky rayon, Volynska oblast)

2.6 Community Projects

CBA aims to improve living condition of local communities and strengthen participatory governance. For this purpose, it supports implementation of local priorities reflected in term of 'micro-projects' or 'community initiatives' through small grants based on equity, productivity, sustainability and cost sharing criteria. During the quarter, a total of 47 community project proposals were processed and approved under following procedural framework.

2.6.1 Preparation of and mainstreaming of community development plan (CDP)

During the quarter, 475 COs developed community development plans as given in Table - VIII. The plans were centred around priorities as follows: medicine - 27%, water supply - 18%, energy saving - 48%, environment - 2%, local transport - 4%.

During the year, 355 COs submitted their priorities to their respective VCs/CCs for approval. Plans concurred by VCs/CCs were then discussed at LDF meetings. Of all the plans discussed, 215 plans were approved by LDFs and recommended for financing (Table - VIII).

Table - VIII: CDP Developed by COs (as of end 2008)

№	Oblast	No of COs with CDPs	Priorities of CDPs						No of CDPs reviewed	No of CDPs approved
			Medicine	Water-supply	Energy Saving	Environment	Local Transport	Other		
1	ARC	35	6	16	8	0	2	0	32	12
2	Chernihivska	26	10	6	10	0	0	0	26	9
3	I-Frankivska	35	10	2	23	0	0	0	35	35
4	Kharkivska	8	0	5	3	0	0	0	0	0
5	Khersonska	40	12	6	22	0	0	0	25	0
6	Khmelnyska	20	2	4	8	3	3	0	20	10
7	Kirovohradska	10	2	2	4	0	2	0	0	0
8	Kyivska	43	13	7	21	2	0	0	43	43
9	Luhanska	39	9	10	20	0	0	0	14	14
10	Lvivska	17	8	0	8	0	1	0	7	3
11	Mykolaivska	0	0	0	0	0	0	0	0	0
12	Odeska	11	3	5	2	1	0	0	11	0
13	Rivnenska	35	10	1	21	0	3	0	20	20
14	Sumska	20	7	8	4	0	1	0	17	0
15	Ternopilka	28	7	4	15	0	2	0	4	1
16	Vinnyska	10	0	2	6	0	2	0	10	10
17	Volynska	25	2	2	21	0	0	0	15	11
18	Zakarpatska	37	13	4	11	4	0	5	37	15
19	Zaporizka	0	0	0	0	0	0	0	0	0
20	Zhytomyrska	39	15	3	20	0	1	0	39	32
Total		475	129	87	227	10	17	5	355	215
		100 %	27%	18%	48%	2%	4%	1%		

2.6.2 Approval of micro-project proposal

During the last quarter of 2008, 47 micro-project proposals were approved by CBA Project. Of them, and 62% belonged to Energy saving, 19% belonged to health purpose, 13% belonged to water supply purpose, 6% - to local transportation (Table – IX).

Table - IX. Typology of MPs

Oblast	# Appr. MPs	# MPs by typology				
		Health	Energy saving	Water supply	Environment	School bus
Chernihivska	2	0	1	1	0	0
I-Frankivska	10	2	8	0	0	0
Khmelnyska	4	0	3	0	0	1
Lvivska	3	2	1	0	0	0
Rivnenska	7	2	5	0	0	0
Ternopilka	1	1	0	0	0	0
Vinnyska	8	0	6	0	0	2
Volynska	2	0	2	0	0	0
Kyivska	3	0	3	0	0	0
ARC	7	2	0	5	0	0
Total #	47	9	29	6	0	3
Total %	100%	19%	62%	13%	0%	6%

Box - 12 . Impact of CBA micro-projects on life of local communities

In Yampil village (Khmelnyska oblast) there was no heating system in local kindergarten. Local budget does not have enough funds to replace the heating system nor introduce some energy-saving measures. Consequently, it was planned to close down the kindergarten. After activation of local community, there is a perspective of replacement of heating system and enlargement of the kindergarten. For this purpose, Co members already collected more than UAH 8'000.

Total cost of 47 approved project is more than UAH 6 mln, average cost of a micro-project being UAH 134'336. According to the cost-sharing arrangement, micro-projects will be co-funded by local budget (51%) with 15% contribution from village/city budget, 34% from rayon budget, 2% from oblast budget. Average input of CO was 10% against 5%. Average CBA share constituted 39%. Moreover, communities managed to attract private sector to co-fund their initiatives (1%). Details are given in Table - X.

Table - X: Micro-project Proposals Processed (as of end 2008)

Oblast	# Approved MPs	Total project cost, UAH	Cost-Sharing Arrangement						Private Sector
			CBA	CO	Local Budget				
					VC	RSA	OSA	Sub-Total	
Chernihivska	2	279798	119926	26449	60651	60954	0	121605	11818
I-Frankivska	10	1076995	536592	61051	102789	376563	0	479352	0
Khmelnyska	4	408475	195880	39473	54992	112580	0	167572	5550
Lvivska	3	441227	183860	24855	23700	207312	0	231012	1500
Rivnenska	7	842731	355360	62223	112472	302125	0	414597	10551
Ternopil'ska	1	118250	59747	17510	40993	0	0	40993	0
Vinnyska	8	1096777	408000	67375	90258	370000	157644	617902	3500
Volynska	2	333096	102000	30163	26497	174436	0	200933	0
Kyivska	3	385634	151502	19451	0	214681	0	214681	0
ARC	7	1330819	319289	296934	409529	305067	0	714596	0
Total	47	6313802	2432156	645484	921881	2123718	157644	3203243	32919
In %			39%	10%	15%	34%	2%	51%	1%

It is expected that at least 40'877 persons will benefit from the realization of the 47 initiatives on improvement of living quality. Of them, 44% are males, 56% are females (Table XI).

Table - XI. Beneficiaries of Community Projects

Oblast	# Approved MPs	No of beneficiaries		
		Total	M	F
Chernihivska	2	550	220	330
I-Frankivska	10	12105	5110	6995
Khmelnyska	4	2532	1033	1499
Lvivska	3	2164	923	1241
Rivnenska	7	7731	3424	4307
Ternopil'ska	1	609	255	354
Vinnyska	8	10641	4839	5802
Volynska	2	595	326	269
Kyivska	3	1800	787	1013
ARC	7	2150	918	1232
Total	47	40877	17835	23042
In %		100%	44%	56%

Box - 13. Fundraising for Financing of CO Projects

In Khmelnytska oblast, Krasnylovskiy rayon, children from 3 villages (Zaktryrychchia, Rublianky and Antonyny) faced difficulties in reaching local school. Local community formed an organization "Antonynskiy Kray" and developed project proposal to purchase a school-bus. Proposal was approved by Local Development Forum and supported by CBA. First tranche was released for purchase of the bus at the end of 2008.

In order to raise money for co-financing, community organized a competition of childrens' drawings/ paintings. This competition also allowed to attract additional funding from local businessmen.

2.6.3 Financing of micro-project proposal

In the IV quarter, financing for released for 12 community projects was done: first tranches were released for 12 projects in ARC and Vinnyska oblast; 3 second tranches were disbursed for micro-projects of ARC. Details are given in Table - XII.

Table - XII. Financing of Micro-projects from CBA

#	Village	CO Name	Project Name	Disbursements			
				1 st Tranche		2nd Tranche	
				UAH	Date	UAH	Date
Autonomous Republic of Crimea							
1	Zvzdne	CO "Zvzdne-L"	Improvement of water supply system	9 180	10-Nov	32130	16-Dec
2	Krasna Polyana	Village Committee "Vidrodzhennya"	Community Health Care Centre	9 180	10-Nov	32130	11-Dec
3	Novokaterynivka	Community Organization "Dzhereltse-2008"	Improvement of water supply system	9 180	10-Nov	32130	11-Dec
4	Nova Derevnnya	Cooperative "Vodogray-Nova Derevnnya"	Improvement of water supply system	9 180	10-Nov		
5	Frunze	Cooperative "Nove Zhyttya"	Improvement of water supply system	9 044	10-Nov		
6	Pervomyske	Cooperative "Omega-2008"	Improvement of water supply and sewerage system	8 093	10-Nov		
7	Vidvazhne	NO "Vidvazhne"	Community Health Care Center	10 000	2-Dec		

#	Village	CO Name	Project Name	Disbursements			
				1 st Tranche		2nd Tranche	
				UAH	Date	UAH	Date
Vinnytska oblast							
8	Obukhiv	Farming Cooperative "Dobrobut-G"	Improvement of Kindergarten	10 200	3-Dec		
9	Strointsy	Ahentsiya Rozvytku Teritorialnoy Gromady of Strointsy Village	Improvement of Kindergarten	10 200	3-Dec		
10	Illiashivka	Ahentsiya Rozvytku Teritorialnoy Gromady of Illiashivka Village	Improvement of Kindergarten	10 200	3-Dec		
11	Teplyk	Ahentsiya Rozvytku Teritorialnoy Gromady "Krok v Maybutne"	Improvement of Kindergarten	10 200	3-Dec		
12	Orativ	Ahentsiya Rozvytku Teritorialnoy Gromady of Orative Village	Improvement of Kindergarten	10 200	3-Dec		

2.7 Communication and visibility

Communication, visibility and public relation (PR) activities are designed as a part of Project implementation strategy with a purpose to maximize transparency about the Project activities and to lobby for the cause it aims to promote. Specific activities include media events, media coverage, web portal, communication dissemination, visibility tools etc.

During the quarter, wider public and potential participants were familiarized with Project activities and plans through local media and CBA web site. Visibility of EU and UNDP was assured by each of communication activities. Details of the activities are described below:

2.7.1 Media coverage

Most of the media coverage was the outcome of media events and participation of local journalists in rayon and village seminars as well as dialogues with community members. During the reporting period, 235 media coverages were registered across Ukraine. It included printed and electronic editions, radio and TV reportages (Table - XIII). Since inception, media coverage of CBA activities amounts to 780, including publications in printed editions (356) and electronic media (206), television (112) and radio reportages (106) (Annex – 10, 12). An extensive use of partners' web resources allowed to efficiently communicate information to target audiences, total of 188 publications of announcements/news items appeared on web sites of OSA/OC, RSA/RC and CBA.

Table - XIII. Media Coverage of CBA Activities during IV quarter

№	Oblast	Coverage		SN	Oblast	Coverage	
		Q-4	2008			Q-4	2008
1	ARC	7	12	14	Lvivska	7	29
2	Cherkaska	0	16	15	Mykolaivska	6	6
3	Chernihivska	4	26	16	Odeska	15	15
4	Chernivetska	5	18	17	Poltavska	3	23
5	Dnipropetrovska	20	24	18	Rivnenska	12	88
6	Donetska	0	0	19	Sumska	17	46
7	Ivano-Frankivska	5	46	20	Ternopil'ska	23	65
8	Kharkivska	21	107	21	Vinnytska	0	5
9	Khersonska	7	27	22	Volynska	21	21
10	Khmeln'ytska	6	23	23	Zakarpatska	8	21
11	Kirovohradska	11	32	24	Zaporizka	21	49
12	Kyivska	8	41	25	Zhytomyrska	0	32
13	Luhanska	8	8		Total	235	780

Box- 14.

Impact of media coverage on project implementation

In Kharkivska oblast, during one of the press-attended meetings with heads of pilot rayons, CBA community development officer presented a brief summary of the project. In one of the rayons, village councils were not yet selected. When this fact was published in local newspaper, a very active reaction of rayon leadership followed, to speed up selection of village councils. "We don't want media to publish that we are lagging behind", - representative of rayon leadership said.

2.7.2 CBA presentation at externally organized events

With a view of disseminating information about CBA Project among interested target groups, its representatives took part in external events to present the initiative and its modus operandi. In the reported period, Project was presented at 50 external events with an audience of 2992 persons (See Annex - 11 for details).

Box - 15 CBA Experience Recommended for Wide Dissemination

In Kirovohrad, CBA representative was invited to participate in the meeting of Oblast Coordination Council on Self-governance, devoted to the topic of *Strategic Planning of the Region's Development*. Presentation of CBA and its activities evoked a vivid discussion among members of the Council, among which were 21 Heads of RC and 4 mayors of big cities. Participants expressed interest in dissemination of CBA activities among other rayons of Kirovohradskaya oblast. Resolution of the forum recommended to involve local communities in the process of drafting of plans and programmes of social-economic development of the territories.

2.7.3 Issuing Regional Newsletters

In order to duly and timely inform local partners/stakeholders as well as participants about progress of CBA activities in the region, a practice of publishing regional newsletters was introduced. Each OIU drafted, published and disseminated copies of the newsletter both electronically (3'552 copies) and printed copies (8'212 copies), to the distribution list including oblast administration and council, rayon administration and councils, village councils, local communities, local media and NGOs (see Table - XIV for details). Newsletters were also placed on CBA web site.

Table - XIV. Publication and dissemination of Regional Newsletters

Oblast	Newsletters per IV quarter			Newsletters per year 2008		
	No of issues published	No of copies printed & distributed	No of copies sent electronically	No of issues published	No of copies printed & distributed	No of copies sent electronically
ARC	1	1	1	1	50	50
Cherkaska	1	50	50	1	50	50
Chernihivska	4	150	300	4	190	400
Chernivetska	1	100	80	1	100	80
Dnipropetrovska	0	0	0	0	0	0
Donetska	0	0	0	0	0	0
Ivano-Frankivska	3	470	16	4	580	32
Kharkivska	1	47	72	1	47	72
Khersonska	1	100	20	2	200	130
Khmelnyska	1	50	50	1	50	0
Kirovohradska	0	0	0	1	100	100
Kyivska	2	270	63	3	720	63
Luhanska	2	480	20	3	580	30
Lvivska	0	0	0	0	0	0
Mykolaivska	2	300	200	2	300	200
Odeska	4	800	10	7	1250	10
Poltavska	2	160	0	2	160	0
Rivnenska	0	0	0	0	0	0
Sumska	2	850	20	3	1550	50
Ternopil'ska	2	160	160	2	160	160
Vinnyska	0	0	0	0	0	0
Volynska	0	0	0	0	0	0
Zakarpatska	1	250	250	3	650	650
Zaporizka	2	200	200	4	1225	1225
Zhytomyrska	0	0	0	1	250	250
Total	32	4438	1512	46	8212	3552

2.7.4 Media Events

In the IV quarter, as programme activities shifted towards community mobilization, less media events took place. During the year, 30 media events were organized in the regions.

Most of rayon seminars were held as media events, this allowed regional units to develop a network of local journalists interested in the project. These contacts were further used to communicate information to the public, as needed. On an ad-hoc basis, media representatives were invited to village council seminars and dialogues with communities. Case of specifically organized media event is quoted in Box- 16.

Box - 16.
Press Conference for Presentation of Regional Annual Report

On 22 December 2008 CBA Community Development Officers initiated the press conference to present annual report on CBA activities and results in Chernivetska oblast. Focal points from OSA and OC were also invited to present their vision of cooperation with the CBA Project. Local media was interested in CBA implementation since the beginning of Project's activities in the region. At the present stage, media representatives were especially interested in the co-financing and the influence of economic crisis on implementation of micro-projects.



Photo 12. Press Conference in Chernivetska OSA

2.8 Advisory and Management

Various activities were carried out during the reporting period to lay foundation for effective operation of the Project activities. These activities are reflected in terms of administrative and financial management, coordination arrangement, and monitoring, advisory support and resource mobilisation as described in details hereunder.

2.8.1 Coordination of CBA at national level

On 9 October 2008, the CBA Project Steering Committee was held. has received the report from the Project team and noted its good achievement and the results. The Steering Committee also took note of some concrete challenges and problems frequently connected with administrative support or support of local authorities. Steering Committee also shared a number of suggestions on how to improve coordination between CBA Project and other initiatives through different mechanisms on the governmental side. In particular, the Project has received suggestions of administrative support from the Secretariat of the Cabinet of Ministers and also the suggestion from the Ministry of Regional Development to make use their of the coordination mechanisms for distribution of information and implementation of the Project in the regions.

Propositions were also received from the Ministry of Agrarian Policy on ways of closer coordination, from the Association of Village and City Councils of Ukraine - on ways of exchange of information about communities which are ready to undertake similar work.



Photo - 13: CBA Steering Committee Meeting

List of participants of Steering Committee is given in Annex -13.

2.8.2 Partnership with national agencies

Following the CBA Steering Committee meeting, the Project team met with focal point of main national-level stakeholders: Ministry of Regional Development and Construction and Department of Regional Policy of the Secretariat of Cabinet of Ministers. Agenda of the meeting presupposed (a) discussion of current challenges of project implementation at regional level, and possible assistance from stakeholders to minimize them; (b) perspectives and mechanisms of further cooperations.

As a result of the meeting, official letter was issued by SCMU to oblast administrations where delays in launching/implementation of the project were observed. Regions reacted with a more active support for CBA.

2.8.3 Coordination with other UNDP-project

Resource person support was provided to UNDP/MGSDP in its effort to introduce community based approach to sustainable development in curriculum of the universities of Ukraine. In this context, IPM Dr. Jaysingh Sah participated in the Inter-University Conference “Local Sustainable Development: Theoretical and Practical Aspects” which was held on 28 November 2008. He shared the global experience of social mobilization to the participants. The objective of this Conference was to ensure wide scientific dialogue on the problems of teaching the community-based sustainable development in the universities and to recommend this course to be included in the list of courses advised by the Ministry of Education and Science of Ukraine.

Also, IPM Dr. Jaysingh Sah participated in the annual meeting of the ‘national forum of partner municipalities’ of UNDP/MGSDP during 11-12 December 2008. During the meeting, Dr. Sah presented CBA project to the participants in light of drawing possible inter-project synergy between the two projects.

2.8.4 Establishing rayon resource centre

To facilitate the work of OIU-team, each partner RSA/RC is expected to depute a staff to form a rayon resource centre and contribute to the task of OIU team. By December 2008, all partner RSAs/RC of targeted 193 deputed their staffs for this purpose. Training was organized for rayon focal points as described in section 2.5.1.

2.8.5 Operational manuals and guidelines

To facilitate the effective implementation of the Project activities, following manuals, guidelines, concept/strategy papers were developed/conceived during October – December, 2008:

CO Manual for local;

Technical Manual for para-technicians of the COs (in process of preparation)

2.8.6 Review and Evaluation

In order to review progress and achievements of each region and to set targets for 2009, two cluster meetings were held during the quarter. CBA staff from 9 oblasts gathered in Yevpatoria (19-20 November) and Ivano-Frankivsk (24-25 November).

2.8.7 Resource mobilisation and utilisation

Besides resource available to CBA from its donors (EU, UNDP), various agencies express their commitment for financial contribution in course of forging partnership with CBA. Level of resources committed so far for CBA Project from various partners and their utilisation is given in Table - XV below.

Table - XV: Resource Availability and Utilisation

SN	Agency	Unit	Resource Provision in 2008		Resource Actually Available	Resource Utilisation	
			Q4	Total		Amount	%
1	European Union	USD			1 252 476.51	1 237 330.58	98.79
2	UNDP	USD			336 000.00	318 802.00	94.88
	Sub-total				1 588 476.51	1 556 132.58	
3	OSAs/OCs	UAH	157 644	157 644		In process	
4	RSAs/RCs	UAH	2 123 718	2 123 718		In process	
5	VCs/CCs	UAH	921 881	921 881		In process	
6	Private sector	UAH	32 919	32 919		In process	
	Sub-total		3 236 182	3 236 182			

Indicated resources of OSA/OC, RSA/RC and VC/CC is a total of sums of their commitments for co-financing of community projects, as indicated in project proposals. Actual amounts are being disbursed and utilized by communities according to individual project implementation plans.

2.8.7 Financial Delivery

Gross delivery of US \$ **1 556 133** was made since the beginning of 2008. Activity-wise delivery is given in Table – XVI.

Table - XVI. Financial Devilery in 2008

№	Key Activities	Budget	Expenditures 2008	Balance	Delivery
		USD	USD	USD	
1	Training of CBA Project staff and national counterparts on community based approach, project strategy and methodology	123 239	118 011	5 228	96%
2	Establish mechanism of participatory planning process at local and regional level	21 400	4 046	17 354	19%
3	Support COs for sustainable management and implementation of self-help initiatives (including seed grants)	189 319	91 086	98 233	48%
4	Establish partnership with oblasts & raiyons administrations, councils and other local stakeholders	53 500	57 637	-4 137	108%
5	Effective Project Management	1 150 933	1 235 937	-85 004	107%
6	PR, Communication and Monitoring Activities	50 086	49 416	670	99%
TOTAL		1 588 477	1 556 133	32 344	98%



CHAPTER III

LESSONS AND OPPORTUNITIES

3.1 Stocking the Experience

3.2 Outlook for future

3.1 Stocking the Experience

- Speed and efficiency of project implementation greatly depends on the degree of **interest of local authorities** and/or availability of enthusiastic officials/leadership at OSA/OC and- RSA/RC. Involvement of local/regional authorities can facilitate project activities in many aspects including increase in the level of trust in the mind of local population since these authorities are perceived as “guarantors” of realization of communities’ initiatives.
- Despite differences in political affiliation, OSA and OC representatives come together to act jointly in favour of the citizens vis-à-vis CBA Project.
- Generally, **communities show great enthusiasm** when it comes the matter of their empowerment, local development and planning. Community members tend to openly demonstrate their interest and enthusiasm in the project, and actively participate in project activities..
- **Main idea of the CBA Project is correctly understood and accepted** by local communities as well as local authorities. As a result, main focus is placed on the creation of a pro-active community and its empowerment. Active participation of communities in solving their own problems is a first and most important step towards sustainable local development.
- **Seminars, trainings and exposure visits** have proved to be an effective way of working with local communities. These activities open up the community members for two way interactive dialogue, mutual trust, understanding and cooperation with OIUs.
- Participation of the **representatives of RSA law/ justice departments, state registrar, rayon tax administration etc to participate in trainings** for local communities turned out to be effective. They clarified requirements as regards CO statute documentation needed for registration.
- Regular and wide **media coverage** of the CBA activities and achievements in the rayons/communities is not only useful for dissemination of information but also it inspires local communities and promotes the spirit of competition among community organizations.
- **Women** are usually most active members of village communities.
- **Pilot communities of CBA** feel themselves special and inspired being involved in such an initiative. They communicate more often with similar pilot communities and receive much higher degree of attention from RSA/RC.
- **Leadership problems** In communities where elected leaders are weak and have no contact with the community members, the community members also tend to be passive and incompetent.
- There is a high probability of negative impact of **political and economic instability** on the formation of COs, community planning and realization of micro-projects. Possible elections to Verkhovna rada are also likely to negatively influence the unity of the community organizations and timely implementation of the local initiatives.
- **Economic crisis** and state budget-2009 poses risk to the co-financing of micro-projects from local budget. Room is to be explored to mobilize resources from oblast-level budget. In this context, emphasis is to be made on systematic informing regional leadership, and deputies of oblast council about the Project and its activities.
- In the process of project implementation, there is a need to create **rayon-level Community Resource Centres**, especially in the rayons remote from regional capital.
- **Empowered communities** are able to influence decision-making processes and development processes at their territories through procedures of common planning.
- Effectiveness of **Local Development Forums** is higher in case by rayon administration/council are involved in its organisation. This reflects the degree of their interest in the Project and allows rayon to feel as a full-fledged partner.
- In the situation where a community perceives a CDOs as its partners rather than a friend, then it seems to gain better understanding about its obligations and responsibilities.
- In rayons where trained **community activists are motivated to serve as resource person and provide the same training to the rest of the community members**, a much higher degree of mastering and understanding the topics of trainings is achieved.
- During **dialogues with communities**, situations should be avoided when a representative of authorities voices his/her vision of the problem that needs to be solved. It is the activist of the community organization who has to take up the initiative. Only in this case will community be focused on a true priority.

Key Challenges and potential threats:

- In some rayons, appointed focal points did not show adequate enthusiasm in cooperating with the Project. This greatly complicated implementation of initiatives in these areas.
- In communities where active leadership is lacking, community often remains disorganized and inactive.
- Limited technical know how at the community level.
- There exists a problem of property right of some micro-project sites that could be reconstructed under the CBA Project, whose documents are lost since post-soviet times. These sites do not belong to anyone but are used for the community needs and are maintained by village councils. Question is to be solved about possibility of financing of such objects by CBA Project.
- Authorities in some oblast/rayon show low enthusiasm in understanding of the idea and methodology of CBA.
- Speed of co-financing from different levels of budget can pose challenge in timely implementation of micro-projects.

Recommendations for immediate action:

- To organise exchange visits for the local authorities and CO-leaders to successful cases/ demonstration sites with an aim of enhancing learning mechanisms .
- To hold learning sessions on computer literacy for CO members
- To hold an inter-regional press-tour, involving different media partners
- To organize regional seminars on technical issues of project preparation and implementation involving representatives of local authorities and the COs.

3.2 Outlook for future

In line with the Project Work Plan and in sequence of the activities being pursued, following activities are --- envisaged for 2009:

- Completing rayon selection and establishing partnership with the selected rayons;
- Completing selection of (1000) VCs/CCs and forging partnership with them;
- Establishing (200) rayon resource centres by developing human resources at RSA;
- Completing development of 1000 COs in selected VCs/CCs and developing their capacity;
- Approving at least 850 micro-projects and funding for their implementation by local communities;
- Widening the horizon of partnership and cooperation with national stakeholders and other sources of funding and synergy;
- Completing establishment of (200) local development forums and (24) oblast coordination council;
- Finalising data base and making wide dissemination of Project related information and experience;
- Holding 2nd Steering Committee Meeting;
- Undertaking mid-term evaluation of the Project performance;
- Enlarging the scale of human resource development within the Project framework



Chapter IV. **ANNEXURE**

- Annex 1. Summary of Regional Launching of CBA Project**
- Annex 2. Summary of Rayon Selection Meetings, IV quarter**
- Annex 3. Summary of Rayon Seminars (since inception)**
- Annex 4. Summary of Selection of VC/CC (since inception)**
- Annex 5. List of Selected Village/City Councils (quarter -IV)**
- Annex 6. Summary Selection of Local Communities**
- Annex 7. Formation of Community Organisation in 2008**
- Annex 8. Summary - Participation in CO Training**
- Annex 9-A. Evaluation of Cluster meeting in Yevpatoria**
- Annex 9-B. Evaluation of Cluster meeting in Ivano-Frankivsk**
- Annex 10. Media Coverage of CBA Activities Registered during 2008**
- Annex 11. Participation of CBA regional coordinators in the external events**
- Annex 12. Summary of Media Coverage per Region**
- Annex 13. List of participants of CBA Steering Committee**

Annex - 1.
Summary of Regional Launching of CBA Project in 2008

№	Oblast	Date of Regional Seminar	Date of Partnership Agreement Signature
1	ARC	23 May	28 July
2	Cherkaska	28 August	28 August
3	Chernihivska	25 April	03 June
4	Chernivetska	25 March	23 June
5	Dnipropetrovska	06 August	*
6	Donetska	18 December	*
7	Ivano-Frankivska	28 February	28 August
8	Kharkivska	25 June	14 August
9	Khersonska	22 May	22 May
10	Khmelnyska	27 March	5 May
11	Kirovohradska	14 March	14 March
12	Kyivska	09 April	24 June
13	Luhanska	22 February	*
14	Lvivska	28 March	28 March
15	Mykolaivska	10 April	30 September
16	Odeska	11 March	*
17	Poltavska	19 February	19 February
18	Rivnenska	13 February	13 February
19	Sumska	20 February	20 February
20	Ternopil'ska	26 March	26 March
21	Vinnytska	02 April	2 April
22	Volynska	14 April	14 April
23	Zakarpatska	21 March	21 March
24	Zaporizka	06 March	1 October
25	Zhytomyrska	26 February	26 March

* Partnership Agreements is under review of OSA/OC

Annex – 2.
Summary of Rayon Selection Meetings, IV quarter (2008)

№	Oblast	Date of Meeting	Representatives of Oblast Authorities	Rayons Selected	Rayons in Reserve
1	Cherkaska	16.10.08	Viktor Pavlyuchenko, Deputy Head, OC Maya Kulik, Director of Unit of External Relations and European Integration, OSA	Horodyschenskyi Zvenihorodskyi Kamyanskyi Umanskyi Talnivskyi Chhyrinskyi Shpolianskyi Kanivskyi	Smilyanskyi Cherkaskyi Hrystynivskyi Katerynopil'skyi
2	Dnipropetrovska	16.10.09	Mykhailo Isachenko, Deputy Head of Department of External Relations, OSA; Oleksandr Maetnyi, Deputy Head of Department of Development of Local Governance, OSA	Vasylkivskyi, Dnipropetrovskyi, Pavlohradskyi, Pokrovskyi, Synelnykivskyi, Sofiivskyi, Tomakivskyi, Yuriiivskyi	Petropavlovskyi

Annex - 3.
Summary of Rayon Seminars (since inception)

SN	Oblast	Seminars held	Total No of participants	No of media	Participation of officials in rayon seminar by no. of events				
					OSA*	OC*	OSA-FP	CBA-CDS	CBA-CDA
1	ARC	8	213	4	1	0	0	1	8
2	Cherkaska	8	274	17	1	0	1	1	8
3	Chernihivska	8	192	16	0	0	8	1	8
4	Chernivetska	8	144	8	0	0	0	2	8
5	Dnipropetrovska	8	198	9	2	0	2	2	8
6	Donetska	0	0	0	0	0	0	0	0
7	I-Frankivska	8	251	16	0	0	0	2	8
8	Kharkivska	8	342	10	2	0	1	2	8
9	Khersonska	8	205	8	0	1	0	1	8
10	Khmelnitska	8	390	17	0	3	0	2	8
11	Kirovohradska	8	292	16	0	2	7	2	8
12	Kyivska	9	266	16	0	0	0	3	8
13	Luhanska	8	135	8	0	0	0	0	8
14	Lvivska	8	266	13	0	0	0	2	8
15	Mykolaivska	8	242	4	0	0	0	2	8
16	Odeska	8	192	6	0	0	0	1	8
17	Poltavska	8	273	4	8	7	0	2	8
18	Rivnenska	8	256	14	0	0	6	4	8
19	Sumska	9	163	7	0	4	0	2	9
20	Ternopiiska	8	329	16	0	0	3	2	8
21	Vinnytska	8	402	12	0	0	8	1	8
22	Volynska	8	338	14	1	1	0	1	8
23	Zakarpatska	8	187	7	0	1	0	2	7
24	Zaporizka	8	174	11	0	0	8	2	8
25	Zhytomyrska	8	242	10	0	0	8	2	8
TOTAL		194	5966	263	15	19	52	42	192

*OSA = oblast state administration; OC = oblast council; OSA-FP = OSA focal point; OC-FP = OC Focal Point;
CBA-CDS = Community Development Specialist of CBA Project; CBA-CDA = Community Development
Assistant of CBA Project*

Annex – 4.
Summary of Selection of VC/CC (since inception)

№	Name of Rayon	No of Rayons	No of applications	No of selected local councils			No of local councils in reserve		
				VC	TC	CC	VC	TC	CC
1	Dnipropetrovska	8	54	38	2	0	11	3	0
2	Cherkaska	8	117	39	0	1	23	0	0
3	Kharkivska	8	111	38	2	0	56	1	0
4	Kirovohradska	8	105	37	3	0	22	2	0
5	Mykolaivska	8	79	35	5	0			
6	Chernivetska	8	104	38	0	2	16	0	0
7	Khmelnyska	8	165	35	5	0	24	0	0
8	Sumska	8	98	34	5	1	23	0	0
9	Volynska	8	117	34	5	1	23	1	0
10	Zakarpatska	8	71	34	5	1	31	0	0
11	ARC	8	74	35	4	1	17	2	0
12	Chernihivska	8	136	32	8	0	16	0	0
13	Ivano-Frankivska	8	150	31	5	4	28	0	0
14	Khersonska	8	61	33	7	0	15	0	0
15	Kyivska	9	138	37	3	4	25	0	1
16	Luhanska	8	71	38	2	0	26	0	0
17	Lvivska	8	112	33	4	3	17	0	0
18	Odeska	8	87	14	26	0	11	6	0
19	Poltavska	8	86	36	4	0	15	1	0
20	Rivnenska	8	100	33	5	2	23	0	0
21	Ternopilska	8	116	34	6	0	27	0	1
22	Vinnytska	8	149	35	5	0	15	1	0
23	Zaporizka	8	62	38	2	0	22	0	0
24	Zhytomyrska	8	115	39	1	0	15	1	0
	Total	193	2478	830	114	20	541	18	2

Annex – 5.
List of Selected Village/City Councils (quarter - IV, 2008)

МИКОЛАЇВСЬКА ОБЛАСТЬ	
Назва району	Відібрані сільради/міськради
Сланецький	Сланецька, Возсіятська, Нововасилівська, Ясногородська, Великосербулівська
Кривоозерський	Кривоозерська, Березівська, Тридубська, Бурилівська, Красненьківська,
Вознесенський	Вознесенська, Прибужанівська, Дмитрівська, Новогригорівська, Воронівська
Веселинівський	Покровська, Кубряцька, Луб'янська, Веселинівська, Новосвітлівська
Березнегуватський	Калузька, Мурахівська, Березнегуватська, Висунська, Новосевастопольська,
Доманівський	Олександрівська, Маринівська, Богданівська, Мостівська, Доманівська,
Очаківський	Острівська, Рівненська, Куцурубська, Парутінська, Козирська,
Снігурівський	Афанасіївська, Павлівська, Баратівська, Нововасилівська, Червонодолинська,

ХАРКІВСЬКА ОБЛАСТЬ	
Назва району	Відібрані сільради/міськради
Нововодолазький	Ордівська, Знамянська, Мелихівська, Ватутіне, Староводолазька
Великобурлуцький	Підсереднянська, Червонохвильська, Приколотнянська, Андріївська, Черненська
Сахновщинський	Новоолександрівська, Олійниківська, Огівка, Нова Чернещина, Сахновщинська
Богодухівський	Павлівська, Шарівська, Петропавлівська, Губарівська, Крисинська
Золочівський	Одноробівська, Перша, Олександрівська, Лютівська, Жовтнева, Золочівська
Ізюмський	Бригадирівська, Левківська, Комарівська, Куньовська, Кам'янська
Первомайський	Олексіївська, Суданська, Киселівська, Верхньоорільська, Красненська
Близнюківський	Острівщинська, Кіровська, Башилівська, Добровільська, Самійлівська

ДНІПРОПЕТРОВСЬКА ОБЛАСТЬ	
Назва району	Відібрані сільради/міськради
Софіївський	Мар'є-Дмитрівська, Девладівська, Миколаївська, Нововасилівська, Кам'янська
Томаківський	Томаківська, Вищитарасівська, Володимирівська, Зорянська, Новокиївська
Васильківський	Павлівська, Зеленогайська, Шевченківська, Дебальцівська, Васильківська
Покровський	Катеринівська, Олександрівська, Березівська, Андріївська, Просянська
Синельниківський	Кислянська, Писарівська, Луб'янська, Михайлівська, Василівська
Дніпропетровський	Новомиколаївська, Балівська, Волоська, Чумаківська, Любимівська
Павлоградський	Богуславська, В'язівська, Межиріцька, Новодачанська, Привовчанська
Юр'ївський	Вербуватівська, Жемчужненська, Олексіївська, Преображенська, Чаплинська

ЧЕРКАСЬКА ОБЛАСТЬ	
Назва району	Відібрані сільради/міськради
Уманський	Вільшанська, В'язівська, Ксаверівська, Мліївська, Зеленодібрівська
Канівський	Боровиківська, Вільховецька, Козацька, Неморозька, Юрківська
Тальнівський	Вербівська, Лузанівська, Косарська, Михайлівська, Баландінська
Чигиринський	Гродзівська, Краснопільська, Іванівська, Дубівська, Бабанська
Звенигородський	Кримківська, Матусівська, Капустинська, Топилянська, Лозуватська
Городищенський	Келебердянська, Яблунівська, Литвинецька, Бобрицька, Чернишівська
Кам'янський	Боровицька, Вершацька, Рацівська, Тинківська, Чигиринська
Шполянський	Білашівська, Веселокутська, Гордашівська, Соколовіцька, Майданецька

КІРОВОГРАДСЬКА ОБЛАСТЬ	
Назва району	Відібрані сільради/міськради
Світловодський	Великоандрусівська, Великоскельовська, Миронівська, Озерська, Федірківська
Новоукраїнський	Ганнівська, Кропивницька, Іванівська, Приютівська, Рівнянська
Маловісківський	Ленінська, Мар'янівська, Паліївська, Якимівська, Смолінська селищна
Петрівський	Петрівська, Водянська, Чечеліївська, Петрівська, Балахівська

КІРОВОГРАДСЬКА ОБЛАСТЬ	
Назва району	Відібрані сільради/міськради
Новомиргородський	Дібрівська, Листопадівська, Мартоноська, Пурпурівська, Петроострівська
Гайворонський	Долинська, Казавчинська, Мощенська, Таужненська, Хашуватська
Бобринецький	Бобринківська, Василівська, Володимиро-Іллінська, Куйбишевська, Микола-Бабанська
Олександрівський	Родниківська, Михайлівська, Несватківська, Розумівська, Вищевещаківська

Annex – 6.
Summary Selection of Local Communities in 2008

SN	Oblast	No. of rayons involved	No. of VC/CC involved	# Communities selected in Q-4	No. of communities selected in 2008	
					For Partnership	For Reserve
1	ARC	8	40	0	40	19
2	Cherkaska	8	40	40	40	17
3	Chernihivska	8	40	4	40	16
4	Chernivetska	8	40	0	40	15
5	Dnipropetrovska	1	1	1	1	1
6	Donetska	0	0	0	0	0
7	Ivano-Frankivska	8	40	0	40	28
8	Kharkivska	8	20	20	20	18
9	Khersonska	8	40	40	40	29
10	Khmelnyska	8	40	0	40	0
11	Kirovohradska	8	40	40	40	1
12	Kyivska	9	41	17	44	21
13	Luhanska	8	40	0	40	26
14	Lvivska	8	40	10	40	7
15	Mykolaivska	8	40	40	40	1
16	Odeska	8	21	19	21	0
17	Poltavska	8	40	40	40	18
18	Rivnenska	8	40	0	40	30
19	Sumska	7	28	28	28	0
20	Ternopil'ska	8	40	40	40	27
21	Vinnytska	8	40	0	40	16
22	Volynska	8	40	34	40	0
23	Zakarpatska	8	40	40	40	0
24	Zaporizka	8	40	0	40	22
25	Zhytomyrska	8	40	0	40	0
	Total	169	791	413	794	276

Annex - 7.
Formation of Community Organisation in 2008

№	Oblast	No of rayons involved	No of VC/CC involved	No of COs			No of h/h in village	Participating H/H		CO members		
				Formed	Enrolled with VC/CC	Legally registered		No	In %	M	F	Total
1	ARC	8	35	35	32	29	12293	9640	78%	12467	16459	28926
2	Cherkaska	0	0	0	0	0	0	0	0	0	0	0
3	Chernihivska	8	40	26	23	2	4893	3327	68%	1969	2950	4919
4	Chernivetska	8	40	18	18	5	3101	334	11%	107	227	334
5	Dnipropetrovska	0	0	0	0	0	0	0	0	0	0	0
6	Donetska	0	0	0	0	0	0	0	0	0	0	0
7	I-Frankivska	3	15	40	10	10	748	599	80%	174	300	474
8	Kharkivska	3	15	15	7	5	9576	8312	87%	4007	8461	12813
9	Khersonska	8	8	40	20	20	15153	2429	16%	1421	2027	3448
10	Khmelnyska	8	40	39	12	7	13630	3533	26%	559	1232	1801
11	Kirovohradska	5	25	20	10	10	8099	1805	22%	605	1406	2011
12	Kyivska	9	41	43	43	38	32157	3183	10%	1310	1873	3183
13	Luhanska	8	32	32	14	11	5288	2537	48%	2567	4048	6615
14	Lvivska	8	37	37	5	5	11292	1583	14%	600	983	1583
15	Mykolaivska	8	40	29	0	10	12500	5240	42%	1218	812	2030
16	Odeska	8	16	15	9	5	9067	1168	13%	216	394	610
17	Poltavska	8	40	33	33	8	19657	3089	16%	1205	1884	3089
18	Rivnenska	8	40	47	44	44	29331	6137	21%	761	1622	2383
19	Sumska	6	28	28	20	16	11732	4626	39%	2045	2587	4632
20	Ternopil'ska	8	40	41	33	31	4629	3472	75%	1365	2188	3553
21	Vinnytska	8	40	11	11	10	11130	8754	79%	431	597	1028
22	Volynska	8	40	37	27	27	12968	1069	8%	561	1060	1 621
23	Zakarpatska	8	40	37	29	15	7017	4912	70%	2011	2901	4912
24	Zaporizka	8	40	39	35	23	21182	4791	23%	2062	3089	5151
25	Zhytomyrska	8	39	39	38	20	12433	1582	13%	593	989	1582
	Total	162	731	701	473	351	267876	82122		38254	58089	96698

Annex - 8.
Summary - Participation in CO Training (in 2008)

№	Oblast	No of trainings	No of participants			Participants - CO members	Participants - local gov-t
			M	F	Total		
1	ARC	12	109	126	235	188	47
2	Cherkaska	0	0	0	0	0	0
3	Chernihivska	15	93	272	365	318	47
4	Chernivetska	15	111	184	295	211	84
5	Dnipropetrovska	0	0	0	0	0	0
6	Donetska	0	0	0	0	0	0
7	I-Frankivska	19	141	247	388	360	28
8	Kharkivska	4	68	86	154	140	14
9	Khersonska	12	205	396	601	407	194
10	Khmelnyska	17	117	279	396	299	97
11	Kirovohradska	9	127	172	299	212	87
12	Kyivska	27	354	495	849	618	231
13	Luhanska	15	42	291	333	168	165
14	Lvivska	8	67	93	160	114	46
15	Mykolaivska	2	16	16	32	32	0
16	Odeska	8	67	80	147	103	44
17	Poltavska	4	20	25	45	39	6
18	Rivnenska	21	229	311	540	442	98
19	Sumska	12	109	135	244	216	28
20	Ternopil'ska	27	202	321	523	382	141
21	Vinnyska	7	151	52	203	143	60
22	Volynska	15	200	208	408	300	108
23	Zakarpatska	20	239	161	400	354	46
24	Zaporizka	6	123	97	220	213	7
25	Zhytomyrska	24	176	484	660	512	148
	Total	299	2966	4531	7497	5771	1726

Annex – 9A.
Evaluation of Cluster meeting in Yevpatoria

Q No.	Question	Unit	No. of responses against possible choices				
			1	2	3	4	5
1	Have you ever participated in trainings before?		Yes, often	Rarely	Never		
		No.	12	3	1		
		%	75%	19%	6%		
2	How satisfied you are with the training?		Not at all	Partly	Mostly	Entirely	
		No.	0	0	6	10	
		%	0%	0%	38%	63%	
3	How interesting and relevant was the training?		Not at all	Partly	Mostly	Entirely	
		No.	0	0	4	12	
		%	0%	0%	25%	75%	
4	Estimate the length of training		Too long	Optimal	Too short	Hard to say	
		No.	1	12	3	0	
		%	6%	75%	19%	0%	
5	Estimate the level of trainer		1 (very bad)	2	3	4	5 (excellent)
		No.	0	0	0	4	12
		%	0%	0%	0%	25%	75%
6	Estimate the quality of handouts		1 (very bad)	2	3	4	5 (excellent)
		No.	0	0	0	10	6
		%	0%	0%	0%	63%	38%
7	Estimate the training techniques and methods		1 (very bad)	2	3	4	5 (excellent)
		No.	0	0	0	2	14
		%	0%	0%	0%	13%	88%
8	Did the training help deepen understanding of the topic?		1 (very bad)	2	3	4	5 (excellent)
		No.	0	0	0	4	12
		%	0%	0%	0%	25%	75%
	Total No. of interviewees	16					

Annex - 9B. Evaluation of Cluster meeting in Ivano-Frankivsk

Q No.	Question	Unit	No. of responses against possible choices				
			1	2	3	4	5
1	Have you ever participated in trainings before?		Yes, often	Rarely	Never		
		No.	8	8	8		
		%	33%	33%	33%		
2	How satisfied you are with the training?		Not at all	Partly	Mostly	Entirely	
		No.	1	0	3	20	
		%	4%	0%	13%	83%	
3	How interesting and relevant was the training?		Not at all	Partly	Mostly	Entirely	
		No.	0	0	3	21	
		%	0%	0%	13%	88%	
4	Estimate the length of training		Too long	Optimal	Too short	Hard to say	
		No.	0	15	6	3	
		%	0%	63%	25%	13%	
5	Estimate the level of trainer		1 (very bad)	2	3	4	5 (excellent)
		No.	0	0	0	2	22
		%	0%	0%	0%	8%	92%
6	Estimate the quality of handouts		1 (very bad)	2	3	4	5 (excellent)
		No.	0	0	1	14	9
		%	0%	0%	4%	58%	38%
7	Estimate the training techniques and methods		1 (very bad)	2	3	4	5 (excellent)
		No.	0	0	0	5	19
		%	0%	0%	0%	21%	79%
8	Did the training help deepen understanding of the topic?		1 (very bad)	2	3	4	5 (excellent)
		No.	0	0	1	7	16
		%	0%	0%	4%	29%	67%
	Total No. of interviewees	24					

Annex – 10
Media Coverage of CBA Activities Registered During 2008

	Oblast	Total Coverage	Newspapers	TV	Radio	Electronic Media	Partners' web sites
1	ARC	12	12	0	0	0	1
2	Cherkaska	16	5	4	0	7	3
3	Chernihivska	26	6	2	6	12	6
4	Chernivetska	18	10	3	0	5	5
5	Dnipropetrovska	24	13	7	0	4	2
6	Donetska	0	0	0	0	0	0
7	Ivano-Frankivska	46	19	3	4	20	19
8	Kharkivska	107	48	14	2	43	21
9	Khersonska	27	22	2	0	3	5
10	Khmelnyska	23	9	2	2	10	10
11	Kirovohradska	32	21	8	2	1	17
12	Kyivska	41	22	12	2	5	1
13	Luhanska	8	3	3	2	0	6
14	Lvivska	29	16	0	1	12	14
15	Mykolaivska	6	3	1	1	1	2
16	Odeska	15	8	3	0	4	11
17	Poltavska	23	11	2	5	5	5
18	Rivnenska	88	23	6	25	34	14
19	Sumska	46	21	0	12	13	13
20	Ternopil'ska	65	18	22	22	3	10
21	Vinnytska	5	5	0	0	0	0
22	Volynska	21	2	5	8	6	12
23	Zakarpatska	21	7	4	4	6	0
24	Zaporizka	49	33	5	4	7	7
25	Zhytomyrska	32	19	4	4	5	4
	Cumulative	780	356	112	106	206	188

Annex – 11
Participation of CBA Regional Coordinators in the External Events

№	Oblast	Date	Event and place	≈ N° of participants
1	ARC	19.11.2008	Donor field visit to CIDP-UNDP, Krasnogvardiyskiy rayon, Zvezdnoe village	45
2	Chernihivska	22.07.2008	"Seminar for village council heads" Chernihivska OC	350
		07.11.2008	"Week of social work" Chernihiv Institute of Law, Social Technologies and Labour	120
3	Dnipropetrovska	12.12.2008	"Information day of EU Programmes in Dnipropetrovsk"; Student Palace	60
4	Kharkivska	16.10.2008	Meeting with Council heads, Chuguiv city, Kharkivska oblast	71
		13.11.2008	Conference "European integration of Ukraine" (Berminvody, Kharkiv oblast)	68
		14.11.2008	Kharkiv National University of Karazin, Videoconference with Brussels "Life quality in NATO countries"	63
		26.12.2008	Seminar Polish-Ukrainian Centre of social education, Kharkiv "EU Projects in Ukraine"	36
		05.11.2008	"European citizen school in Kharkiv"	48
5	Khersonska	18.09.2008	Seminar on cooperation of state and non-governmental establishments in resistance to human traffic, with participation of the Democracy Grants Programme representative of Embassy of the United States in Ukraine, deputy heads of RSA, representatives of coordination councils of RSA of family and demographic development, resistance to human traffic and gender policy (oblast state administration)	20
		17.12.2008	Round table meeting on the outcomes of research "Gender problems in executive authorities, local government bodies" and further cooperation with UNDP projects in Ukraine (oblast state administration)	34
		18.12.2008	NGO of OSA meeting (Oblast State Administration)	42
6	Khmelnyska	25.12.2008	Press-conference in OC/OSA	20
7	Kirovohradska	15.10.2008	Opening of Health centre "Drive" for disabled	80
		29.10.2008	Presentation of the book about history of oblast's rayons "To Remember Native Land"	160
		26.11.2008	Coordination Council meeting on local governance issues with the Head of Kirovograd Oblast Council	50
8	Kyivska	10.10.2008	Meeting in Kyiv-Svyatoshino RSA on planning of NGOs' activities in the rayon	22
		27.10.2008	Round table in the Centre for Social-psychological rehabilitation of Kyiv-Svyatoshino district "Non-governmental organisations and building civil society"	26
9	Luhanska	10.10.2008	Central Economic Department Board of OSA	60
		15.10.2008	Meeting of Regional Coordination Council of OSA	30
		31.10.2008	Seminar in OSA with cities and rayons' leaders of Luhansk oblast	60
		04.11.2008	Seminar in OSA with leaders and experts from economic departments of city councils and state administrations.	60
		17.12.2008	International conference in OSA "Investments in eastern regions"	120
10	Lvivska	20.09.2008	Conference "Agencies for local development in Lviv region"	30
		14.10.2008	Seminar "Transborder projects of EU. The role of partnership of authorities and communities"	20
		04.11.2008	Seminar "Village communities. Village school support. Problems and perspectives"	60
		23.11.2008	Seminar "EU xpert projects"	15
11	Mykolaivska	09.10.2008	Meeting of Rayon State Administration in Oblast State Administration	23
		23.10.2008	City: Oblast State Administration, Investments Forum in Mykolaivska oblast	45

12	Poltavska	16.10.08.	Training "Aspects of organisation of international activities in executive and local authorities. Fundraising: basic notions and principles". Facilitated by German Agency for technical cooperation. OSA office.	25
		23.10.08.	Participation in "Local project creation" Facilitated by German Agency for technical cooperation. OSA office	28
13	Rivnenska	28.11.2008	UFSI training "Social mobilisation" from training course for village heads and community active people, involved in the last year fund programme, Korets city, RSA meeting hall.	26
		06.12.2008	Day of local self-governance (Zarichne urban village)	47
		11.12.2008	UFSI training "Legal regulation of land aspects" from training course for village heads, involved in last year programme, Korets city, RSA meeting hall.	19
14	Sumska	17.10.2008	Meeting with leaders of Burynskiy rayon	15
		23.10.2008	Operative meeting with the head of Central Department of Economy, Mr. O.M. Sitak (Oblast State Administration)	14
		31.10.2008	Meeting with leaders of Okhtyrskiy rayon on project implementation issues	14
		04.11.2008	Meeting with the leaders of Lypovodolynskiy rayon on project implementation issues	12
		21.11.2008	Meeting with deputy Head of OSA, Mr O.M. Tsupro	10
		08.12.2008	Oblast Board on social-economic development in the oblast	68
		11.12.2008	Meeting of financial department leaders of of rayon state administrations and city councils (central Department of Oblast State Administration)	34
15	Volynska	Жов.08	Programme "European space" Volyn oblast television"	3
		28.10.2008	International Economic Forum, Volyn Oblast Council	500
		16.12.2008	Coordination Council with the Head of Volyn Oblast Council, Volyn Oblast Council.	50
		23.12.2008	Volyn Oblast Council session, Volyn Oblast Council	150
16	Zakarpatska	30.10.2008	Launch conference of the Project "Resources centres set up in 4 regions of Zakarpattya border with Rumania", facilitator Association "XXI Century" Uzhgorod city, held in Shayan village, Khustskiy rayon.	56
		07.12.2008	Conference "Establishment of information partnership in non-governmental sector" facilitator KCPD of Uzhgorod city.	28
		04.12.2008	Training "Work in a community", facilitator Ukrainian Fund of Social Investments, Svaliava city	27
		05.12.2008	Training "Work in a community", facilitator Ukrainian Fund of Social Investments, Perechyn city	22
17	Zaporizka	28.11.2008	Zaporizhzhya OIU office. Training on management and planning for experts of external economic activities of OSA.	6
			Total	2992

Annex – 12

Summary of Media Coverage per Region

CHERNIHIVSKA OBLAST

№	Назва видання	Назва публікації та посилання (для ел.ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	"Прес-центр"	ЄС та ООН вчитимуть черкащан розраховувати на власні сили	3.09.08	Презентація проекту. Зміст, завдання та мета проекту. умови участі у проекті для сільських громад.
2	"Вечірні Черкаси"	Євроремонт у черкаських селах	2.09.08	Про підписання трьохсторонньої угоди між представниками Програми розвитку ООН, Черкаською облдержадміністрацією та Черкаською обласною радою про конкурс мікропроектів у рамках проекту МРГ
4	"Шполянські вісті"	Єврокомісія виділить 50 тисяч євро на розвиток Шполянщини	18.11.08	Про презентацію проекту та умови участі в ньому. Перелік районів, що долучилися до проекту і будуть профінансовані.
5	"Шполянські вісті"	Міжнародний проект стартує	12.12.08	Про те, які села Шполянського району будуть залучені до проекту.
Телевізійні репортажі				
1	Уманська телекомпанія	Сюжет у новинах		Про реалізацію проекту на Уманщині.
2	Канівська місцева телекомпанія	Сюжет у новинах		Про проведення семінару для сільських голів.
3	Городищенська місцева телекомпанія	Сюжет у новинах		Про умови участі Городищенського району в проекту.
4	Звенигородська місцева телекомпанія	Сюжет у новинах		Про реалізацію проекту в Звенигородському районі та проведений інформаційний семінар.
Публікації у електронних виданнях (не рахуючи повідомлень на веб сайтах ОДА/ОР/РДА/РР/СВА)				
2	Прес-центр	ЄС та ООН вчитимуть черкащан розраховувати на власні сили// http://www.pres-centr.ck.ua/region/cherkasy/9094	3.09.08	Презентація проекту. Зміст, завдання та мета проекту. умови участі у проекті для сільських громад.
3	"Вечірні Черкаси"	Євроремонт у черкаських селах// http://vechirka.ck.ua/08/09/02/vroremont_u_cherkaskikh_selakh_html	2.09.08	Про підписання трьохсторонньої угоди між представниками Програми розвитку ООН, Черкаською облдержадміністрацією та Черкаською обласною радою про конкурс мікропроектів у рамках проекту МРГ
5	"Шполянські вісті"	Єврокомісія виділить 50 тисяч євро на розвиток Шполянщини// http://ua.od-news.com/index.php?option=com_content&task=view&id=806&Itemid=1	18.11.08	Про презентацію проекту та умови участі в ньому. Перелік районів, що долучилися до проекту і будуть профінансовані.
6	"Шполянські вісті"	Міжнародний проект стартує// http://www.shpola.ck.ua/index.php?option=com_content&task=view&id=397&Itemid=68	12.12.08	Про те, які села Шполянського району будуть залучені до проекту.
7		Замітка http://www.treasury.gov.ua/reg/control/chk/uk/publish/printable_article/162744;jsessionid=DB7D2A4999AD1DACC6C135BFF3FA5AED	19.11.08	Про участь начальника управління казначейства Звенигородського району в семінарі в рамках проекту.
8		Сільським головам - про міжнародний проект http://www.shpola.ck.ua/index.php?option=com_content&task=view&id=338&Itemid=68	2.12.08	Інформація про терміни участі Шполянського району в проекті, про що було повідомлено на семінарі для голів місцевих адміністрацій.

CHERKASKA OBLAST

№	Назва видання	Назва публікації та посилання (для ел.ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	"Чернігівщина"	"Перші ластівки"	11.09.08	"Перші кроки населених пунктів по впровадженню проекту "Місцевий розвиток"
Радіо репортажі				
1	Обласне радіо	Про діяльність Проекту МРГ в Чернігівській області	08.10.08	Мета, принципи, завдання діяльності Проекту в області
2	Обласне радіо	Про діяльність Проекту МРГ в Чернігівській області	15.11.08	Про проведення семінарів в с/р
3	Обласне радіо	Про діяльність Проекту МРГ в Чернігівській області	17.12.08	Про проведення тренінгів, про затвердження перших МПП Громад (подано на розгляд 5, затверджені дві)
4	Срібнянське райрадіо	Репортаж про текучу діяльність відібраних сільрад по впровадженню проекту.	17.09.08	"Перші кроки населених пунктів по впровадженню проекту "Місцевий розвиток, орієнтований на громаду."
Публікації у електронних виданнях (не рахуючи повідомлень на веб сайтах ОДА/ОР/РДА/РР/СВА)				
1	Сайт Газети "Високий ВАЛ"	"Перші ластівки"	02.10.08	Інформація про перші створені ГО в області
2	Сайт Газети "Високий ВАЛ"	Проект місцевий розвиток, орієнтований на громаду проводить початок ГО	17.11.08	Інформація щодо проведення тренінгів для членів ОГ та посадовців РДА та Районних Рад
3	Сайт Газети "Високий ВАЛ"	Підсумок за 08 рік	23.12.08	Підсумки діяльності Проекту в області

DNIROPETROVSKA OBLAST

№	Назва видання	Назва публікації та посилання (для ел.ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	"Вісник"	Проект "Місцевий розвиток, орієнтований на громаду"	01.10.08	Етапи впровадження Проекту у Дніпропетровській області
2	"Зоря"	"Євросоюз стимулює розвиток наших громад"	01.11.08	Репортаж з прес-конференції
3	"Рідний край!"	Проект "Місцевий розвиток, орієнтований на громаду"	07.11.08	Затверджено список з 8 районів нашої області для участі у проекті
4	"Наш край"	"Наші громади може підтримати Європейський Союз"	07.11.08	Про проведення районного семінару у Томаківському районі
5	"Дніпровська зоря"	Презентація Проекту "Місцевий розвиток, орієнтований на громаду"	07.11.08	Про проведення районного семінару у Дніпропетровському районі
6	"Васильківський вісник"	"Інтерес Громади повинен вписуватися в інтереси району"	08.11.08	Про проведення районного семінару у Васильківському районі
7	"Вісті Софіївщини"	"Нові можливості для розвитку"	08.11.08	Про проведення районного семінару у Софіївському районі
8	"Синельниківські Вісті"	"На крок ближче до Європи"	13.11.08	Про проведення районного семінару у Синельниківському районі
9	"Зоря"	"Проект; активізація громади"	18.11.08	Про проведення районного семінару у Дніпропетровському районі
10	"Рідний край"	"Центр заходів - Павлоградський район"	21.11.08	Про проведення спільного районного семінару Павлоградського та Юр'євського районів
11	"Покровський край"	"Запрацював новий спільний проект"	29.11.08	Огляд етапів впровадження проекту СВА
12	"Васильківський вісник"			про проведення семінару у Васильківської селищної раді
13	"Рідний край"			про проведення семінарів в Павлоградському районі
Телевізійні репортажі				
1	Дніпропетровський держ. 51	"Новини"	30.10.08	репортаж з прес-конференції
2	Криворізький телеканал	Репортаж	05.11.08	репортаж про початок у дніпропетровській області проекту СВА та проведення семінару у Софіївському районі

3	Васильківський місцевий канал	"Новини"	05.11.08	репортаж про початок у дніпропетровської області проекту СВА та проведення семінару у Васильківському районі
4	Дніпропетровський держ. 51	"Новини"	10.12.08	репортаж з наради по відборі сільських/селищних рад
5	Дніпропетровський 34 канал	"Новини"	10.12.08	репортаж з наради по відборі сільських/селищних рад
6	Дніпропетровський 23 канал	"Новини"	10.12.08	репортаж з наради по відборі сільських/селищних рад
7	Васильківський місцевий канал			репортаж про проведення семінару у Васильківської селищній раді

IVANO-FRANKIVSKA OBLAST

№	Назва видання	Назва публікації та посилання (для ел.ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	Газета "Народна воля"	ООН хоче інвестувати в села району	19.09.08	Про проект МРГ, участь Надвірнянського району в проекті
2	Газета "Народна воля"	Тисменичанці уже визначились	19.09.08	Про семінар у Тисменичанській сільраді та визначення пріоритетної проблеми для громади села
4	Газета "Народна воля"	ООН хоче інвестувати села району	19.09.08	Про проект МРГ, участь Надвірнянського району в проекті
Друковані публікації				
1	Голос Опілля	Тренінги - тнавчання ініціативних груп	11.10.08	Про проведення тренінгів в Рогатинському районі
2	Край	Визначаються з головними завданнями	24.10.08	Про створені ОГ та пріоритети розвитку громад
3	Галичина	3 офірою ООН	21.10.08	Про проведення тренінгів у Городенківському районі
4	Голос Опілля	Створено Форум місцевого розвитку	01.11.08	Про створення, функція та діяльність ФМР на Рогатинщині
5	Голос Покуття	Курс на розвиток територіальної громади	04.12.08	Про проведення в громадах Снятинського району семінарів та перших діалогів
6	Вільний голос	Тренінги в рамках проекту "Місцеви розвиток, орієнтований на громаду"	15.12.08	Про проведення тренінгів для громади Коломиського району
7	Вільний голос	Засідання Форуму місцевого розвитку	23.12.08	Про засідання ФМР в Коломийському районі
Публікації у електронних виданнях (не рахуючи повідомлень на веб сайтах ОДА/ОР/РДА/РР/СВА)				
1	Прикарпатські громади: участь у проектах ЄС та ООН	http://www.radiosvoboda.org/content/Article/1357505.html	08.12.08	Івано-Франківщина – 40 сільських громад із восьми районів Прикарпаття залучені до проекту. Саме через різноманітні проекти технічної допомоги люди намагаються поліпшити життя у своєму населеному пункті. Водночас з'являється усвідомлення, що громада – це не просто територіальне об'єднання
2	Сільські громади не зважають на кризу	http://galtv.if.ua/news/view/08/06/13/1130/	25.11.08	В Івано-Франківську розпочався дводенний теоретично-практичний тренінг для працівників обласних підрозділів впровадження проекту ЄС та ПРООН МРГ і представників обласних державних адміністрацій західного регіону України.
3	Прикарпатські громади: участь у проектах ЄС та ООН	http://www.vezha.org/news/11177.html	09.12.08	Івано-Франківщина – 40 сільських громад із восьми районів Прикарпаття залучені до проекту Європейського Союзу та Програми розвитку ООН МРГ.
4	Євросоюз подає руку	http://kolomyia.org/se/sites/ko/?nid=9744	12.12.08	Коломийщину відібрано до вісімки районів Прикарпаття, які стали учасниками проекту ЄС та Програми розвитку ООН МРГ. Бюджет проекту – понад 13 млн. євро. У червні проведено перший семінар. Також було підписано угоду між РДА, райрадою в ПРООН про партнерство й оголошено конкурс для участі в проекті. Заявки подали 32 сільські і селищні ради. У серпні проводився фінальний відбір. До проекту включено Пилипи, Рунгури, Жукотин, Голосків, Отинію.

KHARKIVSKA OBLAST

№	Назва видання	Назва публікації та посилання (для ел.ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	газета "ВРЕМЯ"	На Харьковщине будут развивать местные общины	09.09.08	Розповідається про результати відбору районів та фінансування проекту в Харківській області.
2	"Нове життя" (районна газета)		30.09.08	Поміщена інформація про презентацію проекту в Близнюківському районі
3	"МАЯК" (районна газета)		26.09.08	Поміщена інформація про презентацію проекту в Богодухівському районі
4	"Радянський патріот" (районна газета)		19.09.08	Поміщена інформація про презентацію проекту в Великобурлуцькому районі
5	"Обрії Ізюмщини" (районна газета)		26.09.08	Поміщена інформація про презентацію проекту в Ізюмському районі
6	"Вісті Водолажчини" (районна газета)		19.09.08	Поміщена інформація про презентацію проекту в Нововодолазькому районі
7	"Колос" (районна газета)		20.09.08	Поміщена інформація про презентацію проекту в Сахновщинському районі
8	"Зоря" (районна газета)		26.09.08	Поміщена інформація про презентацію проекту в Золочівському районі
9	"Знамя труда" (районна)		27.09.08	Поміщена інформація про презентацію проекту в Первомайському районі
10	Журнал "Аналитик. UA"		09.08	Інформація про проект
11	газета «Слобідський край»	Орієнтовано на громаду	18.10.08	На виїзне засідання в Чугуїв, що проходило під головуванням голови обласної ради С. Чернова, приїхало чимало депутатів облради. У ньому взяли участь представники облдержадміністрації та асистент із розвитку громад Програми розвитку ООН у Харківській області (ПРООН) В. Гусев
12	газета «Слобідський край»	Вибір є. І він за громадами	21.10.08	Першою програмою ООН, що прийшла на територію Харківщини, став проект Євросоюзу та Програми розвитку Організації Об'єднаних Націй (ПРООН) під назвою МРГ. Підписаний угодою про партнерство між ПРООН, Харківською облрадою та облдержадміністрацією 4 вересня 2007 року, він діятиме до 31 грудня 2010 року.
13	газета «Радянський партіот»	МРГ в районі	листопад-грудень 08 (постійно)	Поточна інформація про семінари у сільрадах і зустрічі з громадами Великобурлуцького району
14	газета «Вісті Водолажчини»	МРГ в районі	листопад-грудень 08 (постійно)	Поточна інформація про семінари у сільрадах і зустрічі з громадами Нововодолазького району
15	газета "Маяк"	МРГ в районі	листопад-грудень 08 (постійно)	Поточна інформація про семінари у сільрадах і зустрічі з громадами Богодухівського району
16	газета "Заря"	МРГ в районі	листопад-грудень 08 (постійно)	Поточна інформація про семінари у сільрадах і зустрічі з громадами Золочівського району
17	газета "Знамя труда"	МРГ в районі	листопад-грудень 08 (постійно)	Поточна інформація про семінари у сільрадах і зустрічі з громадами Первомайського району
18	газета «КОЛОС»	МРГ в районі	листопад-грудень 08 (постійно)	Поточна інформація про семінари у сільрадах і зустрічі з громадами Сахновщинського району
Радіо та телевізійні репортажі				
1	Золочівське районне радіо	Репортаж про проведення семінару. Інтерв'ю з асистентами з розвитку	23.09.08	репортаж про проведення семінару. Інформація про проект. Інтерв'ю з асистентами з розвитку
2	ТРК "Сиат" (Ізюмський район)	Репортаж про проведення семінару у	25.09.08	репортаж про проведення семінару. Інтерв'ю з асистентами з розвитку

		м. Ізюм. Інтерв'ю з асистентами з розвитку.		
4	Обласне Телебачення	ток-шоу "Лабіринт" (3 повтори за тиждень)	09.09.08	Дискусія у студії на тему "Європейська Інтеграція". Був представлений проект СВА.
5	новини ТВ "Медіапорт"	Новини (5 разів за вечір)	01.09.08	Бігаюча смужка новин. "На Харківщині розпочато проект ЄС/ПРООН "МРОГ". Сільські громади отримують змогу співфінансувати свої ініціативи"
7	Ток-шоу "Лабіринт" Обласного ТБ	6 основних учасників + глядачі в студії. Грацівник ОПВ Гусев - від ПРООН	14.10.08	Виступ В.Гусева про про проект СВА, що також має на меті європейську інтеграцію
8	Харьковские известия (ТК Р1)	Новини	16.10.08	Про нарад голів райрад області і співпрацю з ПРООН
9	ТВ програма "Влада народу"	телеканал Р1	16.10.08	Про нарад голів райрад області і співпрацю з ПРООН
10	НОВИНИ СІАТ. Телевізійні новини району	Репортаж про хід проекту "МРОГ" в районі.	08.11.08	Про семінар у сільрадах села Куньє, Бригадирівка, Крамарівка
11	Первомайське ТБ	Репортаж про хід проекту "МРОГ" в районі.	07.11.08	Про семінар у сільраді Киселі Первомайського району
12	Золочівські новини	Репортаж про хід проекту "МРОГ" в районі.	23.10.08	
13	Первомайські вісті	Репортаж про хід проекту "МРОГ" в районі.	07.11.08	
Публікації у електронних виданнях (не рахуючи повідомлень на веб сайтах ОДА/ОР/РДА/РР/СВА)				
1	Ура-інформ	http://kh.ura-inform.com/17.10.08/17379.html	17.10.08	Асистент по розвитку громад ПРООН Вячеслав Гусев рассказал, что проект «Местное развитие, ориентированное на громаду» работает в Харьковской области с 08 года. Его приоритетными сферами является здравоохранение, энергосбережения, охрана окружающей среды, коммунальное водоснабжение и коммунальный транспорт
2	Медіа-група "Объектив"	http://www.objectiv.tv/161008/19844.html	16.10.08	Системы местного самоуправления в Украине нужно реформировать, уверены в Европе. Сейчас в стране запустили проект «Местное развитие, ориентированное на громаду». В ней принимают участие 8 районов Харьковской области:
3	Харків - Незабаром	http://kharkov.nezabarm.com.ua/news/?cat=4&id=44326	16.10.08	Системы местного самоуправления в Украине нужно реформировать, уверены в Европе. Сейчас в стране запустили проект «Местное развитие, ориентированное на громаду». В ней принимают участие 8 районов Харьковской области
4	Слобідський край ONLINE	http://slk.kh.ua/view_post.php?id=304	18.10.08	На візні засідання в Чугуїв, що проходило під головуванням голови обласної ради С. Чернова, приїхало чимало депутатів облради. У ньому взяли участь представники облдержадміністрації та асистент із розвитку громад Програми розвитку ООН у Харківській області (ПРООН) В. Гусев
5	Слобідський край ONLINE	http://www.slk.kh.ua/view_post.php?id=328	21.10.08	Першою програмою ООН, що прийшла на територію Харківщини, став проект Євросоюзу та Програми розвитку Організації Об'єднаних Націй (ПРООН) під назвою МРГ. Підписаний угодою про партнерство між ПРООН, Харківською облрадою та облдержадміністрацією 4 вересня 2007 року, він діятиме до 31 грудня 2010 року.
6	Ліга Новини	http://news.liga.net/news/N0842160.html	06.10.08	Программа развития ООН (ПРООН) и ЕС "Местное развитие, ориентированное на общину" начинает свою работу в Харьковской области. Этому была посвящена рабочая встреча с руководителями проекта, которую провел начальник Главного управления внешнеэкономических связей и евроинтеграции Харьковской областной государственной администрации (ОГА) В.Коваленко

7	Top PING	http://mynews-in.net/news/society/08/08/06/1433403.html	06.10.08	Как отметили руководители проекта Вячеслав Гусев и Александр Комаровский, подход, положенный в основу проекта, а именно развитие, ориентированное на общину, предусматривает, что местные общины, органы местной исполнительной власти и самоуправления будут совместно определять приоритеты развития территории,
---	----------	---	----------	--

KHMELNITSKA OBLAST

№	Назва видання	Назва публікації та посилання (для ел.ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	"Красилівський вісник"	Разом дієвіше	19.09.08	Про відбір сільських рад в районі і семінар в Антонінах
2	"Пульс"	"Європейський союз допоможе сільським громадам Славутчини"	25.09.08	Про перспективи впровадження проекту в Славутському районі.
3	"Подільські вісті"	Хмельниччини допомагають ООН і Євросоюз	25.09.08	Про відбір 40 сільських рад, Проведення прес-конференції
4.	"Трудівник полісся"	"Європейський союз допоможе сільським громадам Славутчини"	26.09.08	Про перспективи впровадження проекту в Славутському районі
2	"Красилівський вісник"	Разом дієвіше	19.09.08	Про відбір сільських рад в районі і семінар в Антонінах
3	"Пульс"	"Європейський союз допоможе сільським громадам Славутчини"	25.09.08	Про перспективи впровадження проекту в Славутському районі.
4	"Подільські вісті"	Хмельниччини допомагають ООН і Євросоюз	25.09.08	Про відбір 40 сільських рад, Проведення прес-конференції
...	"Трудівник полісся"	"Європейський союз допоможе сільським громадам Славутчини"	26.09.08	Про перспективи впровадження проекту в Славутському районі
1	"Подільські вісті"	Щорічний звіт голови обласної ради І.В.Гладуняка	07.10.08	Відмічено важливість участі області в Проекті МРГ
2	Красилівський вісник	Обіцяти й виконувати	12.10.08	Про проект "Шкільний автобус" Антонінської с/р
3	Вісти ТП	"Джерело" дасть чисту воду.	11.08	Про проект Улашанівської ОГ "Джерело" і діяльність в рамках проекту МРГ в Славутському районі
4	"Трудівник полісся"	Європейський Союз допоможе сільським громадам Славутчини.	20.12.08	Про тренінг для сільських громад Славутського р-ну
Радіо та телевізійні репортажі				
1	ХОДТРК «Поділля Центр»	Телерепортаж	18-19.09.08	Репортаж в новинах про прес-конференцію щодо відбору 8-ми районів
2	ХОДТРК «Поділля Центр»	Радіорепортаж	18-19.09.08	Репортаж в новинах про прес-конференцію щодо відбору 8-ми районів
3	ХОДТРК «Поділля Центр»	Телерепортаж	18-19.09.08	Репортаж в новинах про прес-конференцію щодо відбору 8-ми районів
4	ХОДТРК «Поділля Центр»	Радіорепортаж	18-19.09.08	Репортаж в новинах про прес-конференцію щодо відбору 8-ми районів
Телевізійні репортажі				
1	Хмельницька ТРК	Новини	25-26.12.08	Інформація про прес-конференцію. Звіт за рік по проекту СВА
2	Телеканал "Місто"	Новини	25-26.12.08	Інформація про прес-конференцію. Звіт за рік по проекту СВА

KIROVOHRADSKA OBLAST

№	Назва видання	Назва публікації та посилання (для ел.ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	"Кіровоградська правда" №67	Проекти для громад: гуртом і батька легше бити!	23.09.08	Про відбір районів, презентацію Проекту в Новомиргородському районі, умови партнерства та очікувані результати впровадження

2	"Честь Хлібороба" №68	Європейці налаштовані допомагати сільській місцевості Бобринеччини	13.09.08	Про участь Бобринецького району в Проекті, зміст та очікувані результати впровадження Проекту, підписання угоди, важливий аспект роботи - переконати людей не бути байдужими
3	"Маловисківські Вісті" №73	Європа дає гроші. Чи візьме їх наша громада?	20.09.08	Про семінар в Маловисківському районі, враження від перегляду документального фільму "На сходинку вище", підписання угоди
4	"Маловисківські Вісті" №74	Участь у проекті Євросоюзу - це перемога району	24.09.08	Про мету і завдання проекту, важливу роль та необхідність мобілізації громад для вирішення проблемних для території питань.
5	"Вперед" № 74	Підписано угоду про співпрацю	16.09.08	Про семінар в Олександрівському районі, представлення Проекту спеціалістами КУП В.Шейгусом та О.Рогозиним. Підписання угоди про партнерство
6	"Новоукраїнські новини" №37	Разом дієвіше	20.09.08	Про відбір району до участі у Проекті, зміст та мету проекту, пріоритетні сфери діяльності, план дій щодо впровадження, переглянуті кіноматеріали, досвід інших областей
7	"Новомиргородщина" №37	Проекти для громад: гуртом і батька легше бити!	20.09.08	Про семінар презентацію Проекту в Новомиргородському районі. Зазначено корисний досвід розвитку громад в інших областях, зокрема, показано у фільмі с. Замглай, про можливість реалізації мікропроектів громад
8	"Гайворонські вісті" №77	Для розвитку громад	16.09.08	Про участь району в Проекті, презентація змісту, мети та планів подальшого розгортання роботи з впровадження Проекту
9	"Трудова слава" № 65	Місцевий розвиток, орієнтований на громаду	27.09.08	Про участь Петрівського району в Проекті, підходи, зміст та очікувані результати впровадження Проекту, оголошення конкурсу сільрад
15	"Кіровоградська правда" №67	Проекти для громад: гуртом і батька легше бити!	23.09.08	Про відбір районів, презентацію Проекту в Новомиргородському районі, умови партнерства та очікувані результати впровадження
16	"Честь Хлібороба" №68	Європейці налаштовані допомагати сільській місцевості Бобринеччини	13.09.08	Про участь Бобринецького району в Проекті, зміст та очікувані результати впровадження Проекту, підписання угоди, важливий аспект роботи - переконати людей не бути байдужими
17	"Маловисківські Вісті" №73	Європа дає гроші. Чи візьме їх наша громада?	20.09.08	Про семінар в Маловисківському районі, враження від перегляду документального фільму "На сходинку вище", підписання угоди
18	"Маловисківські Вісті" №74	Участь у проекті Євросоюзу - це перемога району	24.09.08	Про мету і завдання проекту, важливу роль та необхідність мобілізації громад для вирішення проблемних для території питань.
19	"Вперед" № 74	Підписано угоду про співпрацю	16.09.08	Про семінар в Олександрівському районі, представлення Проекту спеціалістами КУП В.Шейгусом та О.Рогозиним. Підписання угоди про партнерство
20	"Новоукраїнські новини" №37	Разом дієвіше	20.09.08	Про відбір району до участі у Проекті, зміст та мету проекту, пріоритетні сфери діяльності, план дій щодо впровадження, переглянуті кіноматеріали, досвід інших областей
21	"Новомиргородщина" №37	Проекти для громад: гуртом і батька легше бити!	20.09.08	Про семінар презентацію Проекту в Новомиргородському районі. Зазначено корисний досвід розвитку громад в інших областях, зокрема, показано у фільмі с. Замглай, про можливість реалізації мікропроектів громад
22	"Гайворонські вісті" №77	Для розвитку громад	16.09.08	Про участь району в Проекті, презентація змісту, мети та планів подальшого розгортання роботи з впровадження Проекту
23	"Трудова слава" № 65	Місцевий розвиток, орієнтований на громаду	27.09.08	Про участь Петрівського району в Проекті, підходи, зміст та очікувані результати впровадження Проекту, оголошення конкурсу сільрад

24	"Вісті Світловодщини" №39	Проект, спрямований на покращення життя громади	25.09.08	Досвід набутий громадами під час роботи з проектами в рамках УФСІ буде мати продовження.
25	"Новомиргородщина" №42	Хочемо і будемо жити краще!	25.10.08	Про зміст і напрямки мікропроектів , які обрали 5 громад району
26	"Новомиргородщина" №47	Що написано пером, втілює задум громади	28.11.08	Про тренінг для організацій громад і представників органів самоврядування з питання ефективного управління ОГ
27	"Трудова слава" №83	Підтримка місцевих громад"	25.11.08	Про результати зустрічей з громадами-учасниками проекту та всебічну підтримку з боку місцевих органів влади
28	"Народне слово" №134	Працювати з поглядом у завтра	29.11.08	Про роль громад у стратегічному плануванні розвитку територій
29	"Народне слово" №137	Жити не лише сьогоднішнім днем	06.12.08	Про роль і участь громад у вирішенні проблем територій
30	"Зовнішсервіс" №2-3	Розпочато впровадження Проекту МРГ	17.12.08	Проект сприятиме зміцненню міжнародних зв'язків
Телевізійні репортажі				
1	Обласна телерадіокомпанія	Інформаційна програма " День за днем"	26.11.08 27.11.08	Репортаж із засідання Координаційної ради з питань місцевого самоврядування при голові Кіровоградської обласної ради .Виступ асистента Т.Головченко про Проект та роль громад у розвитку територій
2		Кіровоградський прес-клуб реформ	6.12.08 7.12.08	Засідання до дня місцевого самоврядування. Про хід впровадження в області Проекту СВА
3	ТРК "Стимул"	Інформаційна програма "Новини дня"	26.11.08 27.11.08	Репортаж із засідання Координаційної ради з питань місцевого самоврядування при голові Кіровоградської обласної ради
4	Телекомпанія ТТV	Інформаційний випуск " ТTV плюс"	26.11.08 27.11.08	Репортаж із засідання Координаційної ради з питань місцевого самоврядування при голові Кіровоградської обласної ради .Виступ асистента Т.Головченко про Проект та роль громад у розвитку територій
10	ТРК " Веселка" м.Світловодськ	Вечерній випуск новин	23.09.08	Репортаж про районний семінар презентацію Проекту
11	ТРК " Веселка" м.Світловодськ	Вечерній випуск новин	23.09.08	Репортаж про районний семінар презентацію Проекту

КHERSONSKA OBLAST

№	Назва видання	Назва публікації та посилання (для ел.ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	Новотроїцька районна газета "Трудова слава"	"Хто співпрацюватиме з проектом"	24.09.08	Новотроїцький район на конкурсній основі здобув право на участь у спільному Проекті ЕС та ООН.
2	Новотроїцька районна газета "Трудова слава"	"Доречна допомога".	24.09.08	Про семінар в с.Володимиро-Іллінка Новотроїцького району
3	Обласна газета "Новий формат"	"Горностаевский получит денег от ООН"	24.09.08	Про конкурсний відбір населених пунктів району
4	Міська газета "Херсон-Маркет плюс"	"Нам допоможуть японці"	18.09.08	Про участь району у програмі "Кусаноне" Посольства Японії та проекті Програми розвитку ООН та ЕС МРГ
5	громадсько-політична газета "Високе поле"	"Новий етап впровадження проекту місцевого розвитку громад"	03.10.08	29 вересня і 1 жовтня обласний підрозділ впровадження Проекту провів у відібраних населених пунктах семінари
6	громадсько-політична газета "Новий час"	5 сільських рад Білозерського району беруть участь в Проекті МРГ	9.10.08	7 жовтня 08 р в РДА відбулась робоча нарада з питань участі 5 сільрад в Проекті
7	"Голопристанський вісник"	Співпраця з ООН	24.10.08	В рамках Угоди про партнерство між Програмою ООН та Голопристанською РДА в вересні проведені виїзні семінари-презентації Проекту
8	громадсько-політична газета "Новий час"	Євросоюз- шлях до демократії на Херсонщині	30.10.08	В рамках проведення Європейського тижня місцевої демократії підписано угоду про партнерство між Високопільськими РДА, РР та Програмою розвитку ООН МРГ

9	"Голопристанський вісник"	На вірному шляху	19.12.08	Розпорядженням голови РДА від 5 грудня утворено Форум місцевого розвитку Голопристанського району. Минулого четверга на засіданні першого Форуму було прийнято резолюцію.
10	Горностаївська газета "Сільські новини"	рубрика "Для розвитку громад"	22.11.08	Про реалізацію проекту МРГ у Горностаївському районі
11	Горностаївська газета "Сільські новини"	рубрика "Для розвитку громад"	27.09.08	Про реалізацію проекту МРГ у Горностаївському районі
Публікації у електронних виданнях (не рахуючи повідомлень на веб сайтах ОДА/ОР/РДА/РР/СВА)				
2	09.09.08	http://www.mobus.com/127207.html		За підтримки Євросоюзу та ООН, про конкурсний відбір сільських рад у Голопристанському районі
3		http://www.politics.kherson.ua/?&lang=ukr&lim_beg=255&sdate_b=nomatter&sdate_e=nomatter&doc_topic=709 - сайт ХОО КВУ "Херсонщина Політична"		Херсонська область підписала партнерську угоду з Програмою розвитку ООН

KYIVSKA OBLAST

№	Назва видання	Назва публікації та посилання (для ел.ЗМІ)	Дата	Короткий зміст
Друковані публікації				
13	Міський районна газета "Перемога" № 95 (9688) від 10.09.08, м. Фастів	Багата Європа не хоче мати бідних сусідів	10.09.08	Про нараду по відборі сільрад в Київській ОДА та розпочаток діяльності у Фастівському районі
14	Міський районна газета "Перемога" № 96 від 17.09.08, м. Фастів	Міжнародний проект на службу Фастівщини	17.09.08	Місцевий розвиток набуде динаміки, якщо громада почуватимеся господарем
15	"Провінція post" №36(524), Сквирський район	Проект МРГ працює	18.09.08	Про хід впровадження Проекту СВА у Сквирському районі, нараду з відбору сільрад в Київській ОДА 08.09.08
16	Фастівська міський районна газета "Перемога" №92 (9685) від 19.09.08	До відома учасників Проекту МРГ	19.09.08	Оголошення про відбірні сільради у Вастівському районі
17	"Вісник Сквирщини" №68(10068)	Пристипили до роботи громади п'яти сіл району	20.09.08	Про семінари в сільрадах та початок навчання обраних громад, визначення першочергових проблем.
18	"Ржищів" №36(480)	Європа сприяє розвитку місцевих громад в Україні	26.09.08	Про хід впровадження Проекту СВА в київській області і зокрема в м. Ржищів
19	Вісник Сквирщини №77 (10077) від 25.10.08	Триває робота над втіленням конкретних ініціатив	25.10.08	Про тренінги в Сквирському районі
20	"Вісник Кагарличини №87 (9901) від 28.10.08	Від намірів - до конкретних справ	28.10.08	Відвідування громад Кагарлицького району, заміна с. Гребені
21	"Вісник Переяславщини" 21 жовтня 08 року	З допомогою Євросоюзу в Єрківцях хочуть розпочати заміну водопроводу	21.10.08	Про зустріч з громадою с. Єрківці
22	"Вісник Сквирщини" №80 (10080) від 05.11.08	Форум місцевого розвитку району - за конкретні позитивні зміни у громадах шляхом співпраці з ЄС/ПРООН	05.11.08	Про ФМР в Сквирському районі
23	"Миронівський край" №88 (9024) від 08.11.08	Громадські ініціативи отримують підтримку	08.11.08	Про хід впровадження Проекту в районі, перспективи громад
Телевізійні репортажі				
10	Ставище_ТРК Грант	Інформаційний вісник	25.09.08	Про семінари в сільрадах Ставищенського району
11	Переяслав-Хмельницький-телебачення	Інформаційна програма "Огляд новин"	16.10.08	Про семінари в сільрадах Переяслав-Хмельницького району
12	Переяслав-Хмельницький-телебачення	Інформаційна програма "Огляд новин"	16.10.08	Про діалог з громадою с.Ковалин
Радіо репортажі				
1	Сквирське районне радіо	Інформаційна програма	20.09.08	Про поїздки з 1-м заст. голови РДА Гриша В.В. по громадам району
2	Сквирське районне радіо	Інформаційна програма	27.09.08	Зустрічі з громадами, загальні збори по Проекту

				МРГ
3	Сквирське районне радіо	Інформаційна програма	18.10.08	Тренінгова програма для 5 громад району
4	Сквирське районне радіо	Інформаційна програма	25.10.08	Тренінги в районі
5	Сквирське районне радіо	Інформаційна програма	08.11.08	Про ФМР в Сквирському районі
6	Кагарлицьке радіо	Інформаційна програма	14.11.08	Про хід впровадження Проекту СВА в Кагарлицькому районі
7	Сквирське районне радіо	Інформаційна програма	15.12.08	Про ФМР в Сквирському районі
8	Обласне радіо	Інформаційна програма	16.12.08	Про проведення ФМР в Миронівському районі. Були названі сільради та МПП громад.

LUHANSKA OBLAST

№	Назва видання	Назва публікації та посилання (для ел.ЗМІ)	Дата	Короткий зміст
Друковані публікації				
4	Вісник Старобільщини	"Несить і Вам допоможуть"	07.10.08	про тренінг по ефективності організації громад та планування їх діяльності
5	Обласний щотижневик "Гривна плюс" №46 (355)	"Залучення інвестицій у східні регіони"	17.12.08	Про виступ на конференції щодо необхідності мобілізувати ресурси громад шляхом самоорганізації та залучення фондів міжнародної технічної допомоги
6	Вісник Біловодщини № 104	"Місцевий розвиток орієнтований на агроадаму"	24.12.08	Про форум місцевого розвитку в Біловодському районі
Телевізійні репортажі				
1	ЛКТ	Новини - колегія Головного управління економіки ОДА	10.10.08	результати по Проекту
2	ІРТА	Новини Старобільщини, рубрика "Репортер"	07.10.08	сюжет про тренінг по ефективності організацій громад та плануванні їх діяльності
3	ІРТА	Новини Старобільщини, рубрика "Репортер"	22.10.08	сюжет про тренінг по розробці мікропроектних пропозицій та поданню їх на фінансування до Проекту
Радіо репортажі				
1	Радіо Станіці Луганської	новини	03.10.08	про тренінг по ефективності організації громад та плануванню їх діяльності
2	Радіо Станіці Луганської	новини	12.11.08	Про форум місцевого розвитку в СтЛуганській райдержадміністрації

LVIVSKA OBLAST

№	Назва видання	Назва публікації та посилання (для ел.ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	Яворівщина - районний часопис Яворівського району	Розвиток, орієнтований на громаду.	19.09.08	Висвітлення інформації про результати візитів в сільські ради та громади.
2	Бойківщина	Усе залежить від громади	20.09.08	Висвітлення інформації про результати візитів в сільські ради та громади.
9	Яворівщина - районний часопис Яворівського району	Розвиток, орієнтований на громаду.	19.09.08	Висвітлення інформації про результати візитів в сільські ради та громади.
10	Бойківщина	Усе залежить від громади	20.09.08	Висвітлення інформації про результати візитів в сільські ради та громади.
11	Воля Народу	Переможці конкурсу визначені	21.08.08	Висвітлення інформації про результати відбору сільських рад.
12	Новий час - Районний часопис Жидачівського району	Пять територіальних громад району зможуть за кошти ООН покращити своє життя	10.10.08	Висвітлення інформації про перші діалоги в громадах
13	Голос Самбірщини-Районний часопис Самбірського району	Представники нового проекту ЄС і ООН заприятелювали з місцевими громадами	10.10.08	Висвітлення інформації про результати навчання представників громад.
14	Наш край - Районний часопис Мостиського району	Навчання громад	14.10.08	Висвітлення інформації про створення Форуму місцевого розвитку
15	Нова Доба - Районний часопис Перемишлянського району	Головою Фонду в Уневі обрали священника	17.10.08	Створення ОГ в селі Унів в рамках Проекту СВА
16	Наш край - Районний часопис Мостиського району	Про розвиток Мостищини	28.10.08	Висвітлення інформації про створення Форуму місцевого розвитку

17		5 сільських рад навчили правильно витратити гроші ООН та ЄС	01.10.08	Висвітлення інформації про результати навчання представників громад.
18	Наш край - Районний часопис Мостиського району	Мостиські громади підписують перші договори про співпрацю з Проектом ЄС/ПРООН	19.12.08	Про результати роботи Проекту СВА в районі та затвердження 2-х проектів громад Циків та Арламівська Воля.
19	Нова Доба - Районний часопис Перемишлянського району	Перший договір громади про співпрацю з Проектом ЄС/ПРООН	12.12.08	Про результати роботи Проекту СВА в районі та затвердження проекту громади села Унів.
Публікації у електронних виданнях (не рахуючи повідомлень на веб сайтах ОДА/ОР/РДА/РР/СВА)				
9	http://www.zik.com.ua	5 сільських рад навчили правильно витратити гроші ООН та ЄС	01.10.08	В 5 сільських рад району, які стали переможцями конкурсу – Домажирській, Старичівській, Прилбичівській, Чернильській та Краковецькій – відбулися семінари. Одне із основних питань, яке виникло під семінарів – механізм використання коштів та внесок громади.
10	http://www.zik.com.ua	Мостиський та Яворівський райони дружно помандрували до Євросоюзу та ООН	20.11.08	Продовжується впровадження спільного Проекту Євросоюзу та Програми розвитку ООН МРГ в Яворівському та Мостиському районах Львівської області. Зокрема, на Яворівщині відбулося навчання громад, які беруть участь у цьому спільному проекті – мешканці Прилбичів та Морянів (Краковецька сільська рада) відвідали три семінари. Активістів-селян обрано зборами сіл
11	http://www.zik.com.ua	25-26 листопада в Івано-Франківську тренінг з впровадження проекту ЄС та ПРООН "Місцевий розвиток, орієнтований на громаду"	26.11.08	25-26 листопада в приміщенні Івано-Франківської ОДА відбувся теоретично-практичний тренінг для працівників обласних підрозділів впровадження проекту ЄС та ПРООН МРГ та представників ОДА західного регіону України.
12	http://www.zik.com.ua	Мостиський районний бюджет допомагає ООН профінансувати зведення двох сільських медичних закладів	19.12.08	У Мостиському районі Львівської області реалізується проект під егідою ООН МРГ. Ним, зокрема, передбачено будівництво фельдшерсько-акушерських пунктів в селах Циків та Арламівській Волі.

МЬКОЛАІВСКА ОБЛАСТ

№	Назва видання	Назва публікації та посилання (для ел.ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	Журнал "Ініціатива"	Перспективи для миколаївських громад	26.12.08	про відбір ср для учасі у проекті
2	газета "рідний причал"	Проект ПРООН у миколаївській області	23.12.08	стаття і фото проведення діалогу у громаді
3	Еланецка газета	Про кроки впровадження проекту	02.12.08	про хід виконання проекту : про проведення діалогів у громадах, визначення проблем
Телевізійні репортажі				
1	Новини Миколаїва	інтерв'ю з начальником управління зовнішньо економічних зв'язків Чичкалюк Т.О.	29.10.08	про підписання угоди на рівні області та ПРООН і зобов'язання в рамках проекту
Радіо репортажі				
1	Радіо ФМ (у миколаївській області)	Прямий ефір - питання розвитку області	21.11.08	про проект МРГ у Миколаївській області
Публікації у електронних виданнях (не рахуючи повідомлень на веб сайтах ОДА/ОР/РДА/РР/СВА)				
1	Інтернет газета ГОРОД N	публікація про проведення презентації про Проект для представників НУО	22.10.08	детально про проект і відібрані райони
2	Pravda.mk.ua	стаття в електронній газеті	22.09.08	Висвітлення проведеної презентації про розпочаток діяльності проекту СВА для лідерів НУО

VINNYTSKA OBLAST

№	Назва видання	Назва публікації та посилання (для ел. ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	Газета обласної ради "Вінниччина"	Людини на своєму місці ..."	09.09.08	деякі сільські голови незважаючи на скрутну ситуацію в своїх голмадах знають як залучити кошти. Сільська громада під керівництвом Миколи Арнаута, відповідально віднеслась до підготовки проектної заявки на участь в проєкті "Місцевий розвиток орієнтованих на громаду" і була відібрана в п'ятірку сільських рад Мурованокуриловецького району. Крім того ця громада була визначена пілотною.
2	Обрії Оратівщини	Як вирішуються проблеми громади		Керівництво області розуміючи необхідність економічного та соціального розвитку громади ініціює та підтримує протягом 5 років проєкти та конкурси направлені на розвиток громад. В цьому році розпочався ще один проєкт в Вінницькій області. Участь в ньому бере п'ять громад Оратівського району, які були відібрані на конкурсній основі. Участь і цій програмі дає можливість залучити кошти в сумі 50 тис. грн. при цьому необхідно забезпечити співфінансування проєктів не меншою сумою. Визначено також пілотну громаду - це Оратівська селищна рада, по цій громаді вже в цьому році планується профінансувати проєкт розвитку громади.
3	Газета обласної ради "Вінниччина"	Людини на своєму місці ..."	09.09.08	деякі сільські голови незважаючи на скрутну ситуацію в своїх голмадах знають як залучити кошти. Сільська громада під керівництвом Миколи Арнаута, відповідально віднеслась до підготовки проектної заявки на участь в проєкті "Місцевий розвиток орієнтованих на громаду" і була відібрана в п'ятірку сільських рад Мурованокуриловецького району. Крім того ця громада була визначена пілотною.

POLTAVSKA OBLAST

№	Назва видання	Назва публікації та посилання (для ел.ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	Оржицькі вісті	"Проект Місцевий розвиток, орієнтований на громаду в районі діє"	25.10.08	Щодо провадження Проєкту в громадах
Радіо репортажі				
1	Репортаж в новинах	Оржицька районна радіостанція	18.10.08	Про семінари в сільських радах
2	Репортаж в новинах	Семенівська радіостанція	07.10.08	Про семінари в сільських радах

ODESKA OBLAST

№	Назва видання	Назва публікації та посилання (для ел.ЗМІ)	Дата	Короткий зміст
Друковані публікації				
5	Дружба	Инициатива не наказуема	07.11.08	Ход реализации проекта в Болградском районе
6	Панорама	Диалог состоялся, работа продолжается	07.11.08	Проведение диалогов в 2-х громадах Болградского района
Телевізійні репортажі				
1	ТРК "ГЛАС"	Передача "Аграрний сектор"	3-9.13 (20 випусків)	Візит посла Євросоюзу до цільової громади проєкту
2	ТРК "ГЛАС"		25.12.08	Прес-конференція начальника управління зовнішньоекономічних зв'язків (в т.ч. - інформація про проєкт)
Публікації у електронних виданнях (не рахуючи повідомлень на веб сайтах ОДА/ОР/РДА/РР/СВА)				
1	Інформаційне видання "ЕХО"	Сельские громады Болграда намерены самоорганизоваться для реализации проекта ЕС и Программы развития ООН	01.11.08	http://eho-ua.com/08/11/01/selskie_gromady_bolgrada_nameren_y_samoorganizovatsja_dlja_realizacii_proekta_es_i_programmy_razvitiya_oon.html

RIVNENSKA OBLAST

№	Назва видання	Назва публікації та посилання (для ел.ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	Громадсько-політичний тижневик Радивилівського району "Прапор перемоги"	Сарненці ділилися... Європейським досвідом	03.10.08	Розповідь про тренінг для районних контактних осіб з 8 областей, що відбувся у Сарнах у рамках проекту СВА
2	Млинівський тижневик "Влада і час"	На раду від громади	04.12.08	Підсумки проведеної громадами роботи у рамках проекту СВА, інформація про тренінгові навчання для активістів ОГ, що відбулися у районі
Радіо репортажі				
1	Заріченське місцеве радіомовлення	Інтерв'ю після завершення засідання ФМР	10.10.08	Про запровадження ФМР, як механізму планування знизу доверху, його цілі, плани та розглянуті питання
2	Заріченське місцеве радіомовлення	Інтерв'ю із лідерами ОГ	10.10.08	Про діяльність і співпрацю із Проектом СВА поділились Лідер ОГ "Струмочок" Т.Мініч та активіст ОГ "Мрія" В.Свирид, які відмітили велику перспективу та активність людей.
3	Рокитнівське місцеве радіомовлення	Інтерв'ю контактної особи від РДА Таргонського Г.М.	10.10.08	Про стан впровадження Проекту МРГ в Рокитнівському районі. Недоліки та успіхи на прикладі Масевицької громади
4	Рокитнівське місцеве радіомовлення	Інтерв'ю після завершення засідання ФМР	12.10.08	Про запровадження ФМР, як механізму планування знизу доверху, його цілі, плани та розглянуті питання
5	Рокитнівське місцеве радіомовлення	Про ОГ "Прометей" смт.Томашгород	28.10.08	Співпраця із міжнародними донорами, Проектом ЧПВР ПРООН. Співпраця із Проектом СВА та плани розвитку
6	Рокитнівське місцеве радіомовлення	Підготовка МПП	07.11.08	Стан підготовки МПП в ОГ району та затвердження МПП ОГ "Відродження" с.Масевичі по енергозбереженню в місцевій школі
7	Рокитнівське місцеве радіомовлення	Підсумки діяльності за рік	25.11.08	Круглий стіл при голові РДА та відвідання ОГ "Надія" с.Хміль
8	Радивилівське місцеве радіомовлення	Новини за тиждень	31.10.08	Інтерв'ю з асистентом з розвитку громад щодо проведених у районі заходів та подальшої активності громад у рамках проекту СВА
9	Гоцанське місцеве радіомовлення	Про установче засідання Форуму місцевого розвитку Гоцанського району	10.11.08	Інтерв'ю з асистентом з розвитку громад стосовно завдань та подальшої причетності Форуму до розвитку територіальних громад та розв'язання місцевих проблем
10	Корецьке місцеве радіомовлення	Про перше засідання Форуму місцевого розвитку Корецького району	12.11.08	Інтерв'ю з асистентом з розвитку громад стосовно призначення цього колегіального органу та його подальшої роботи

SUMSKA OBLAST

№	Назва видання	Назва публікації та посилання (для ел.ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	"Вишневий цвіт" (Охтирський район)	Вікно в Європу	22.09.08	Інформація за результатами відбору сільських рад
12	Газета «Наш край»(Липоводолинський район)	Чотири «П», що заважають розвитку громади або Чи зуміємо реалізувати проекти в районі?	15.12.08	Про реалізацію проекту в районі.
13	Газета «Наш край»(Липоводолинський район)	Надія на проєкт єврокомісії і ПРООН.	17.12.08	Про втілення проекту в Байрацькому ФАПі.
14	Газета «Наш край»(Липоводолинський район)	Люди налаштовані здійснити перетворення на краще у своїх громадах.	20.12.08	Що зроблено вже по проєктах.
15	„Голос часу” (Ямпільський район)	„Щоб життя сільських громад стало кращим”	08.10.08	Про діяльність проекту в Ямпільському районі
16	Районна газета «Рідний край»	Ініціативні громади п'яти сільських рад Буринщини отримують фінансову підтримку від ЄС та ООН	22.10.08	В матеріалі висвітлено значення проекту, його основні напрямки та інформація про учасників
17	Новини Тростянецьчини (Тростянецький район)	Громади визначилися з пріоритетами	03.12.08	Про проведення перших діалогів у громадах Тростянецького району

18	Районна газета «Ворскла» (Великописарівський район)	МРГ	04.10.08	про відбір сільських та селищних рад для впровадження проекту "Мсцевий розвиток, орієнтований на громаду"
19	Новини Тростянецьчини (Тростянецький район)	"Громада визначає пріоритети"	07.11.08	Про проведення першого діалогу з громадою с. Буймер Тростянецького району.
20	"Вишневий цвіт" (Охтирський район)	Проект СВА	14.11.08	про проведення тренінгів для громад Охтирського району
21	"Перемога" (Краснопільський район)	Пріоритети громад	15.10.08	Про визначення пріоритетів громад Тростянецького району
Радіо та телевізійні репортажі				
1	Тростянецьке районне радіо		03.09.08	Про участь сільських рад Тростянецького району у Проекті СВА
2	Краснопільське районне радіо		19.09.08	Про проведення перших зустрічей у сільських радах Краснопільського району
3	Липоводолінське районне радіо	повідомлення у випуску новин	10.09.08	Про участь сільських рад Липоводолінського району у Проекті СВА
4	Тростянецьке районне радіо	повідомлення у випуску новин	03.09.08	Про участь сільських рад Тростянецького району у Проекті СВА
5	Краснопільське районне радіо	повідомлення у випуску новин	19.09.08	Про проведення перших зустрічей у сільських радах Краснопільського району
6	Липоводолінське районне радіо	повідомлення у випуску новин	10.09.08	Про участь сільських рад Липоводолінського району у Проекті СВА
8	Тростянецьке районне радіо	повідомлення у випуску новин	07.11.08	про проведення перших діалогів у громадах Тростянецького району
9	Краснопільське районне радіо	повідомлення у випуску новин	15.12.08	про стан реалізації проекту в районі
10	Липоводолінське районне радіо	повідомлення у випуску новин	16.12.08	про стан реалізації проекту в районі
11	Охтирське районне радіо	повідомлення у випуску новин	13.11.08	про навчання громад
12	ВВС та радіо ЕРА	радіофір за участю представників обласного керівництва	05.12.08	про місцеві проблеми та впровадження проекту в області та започаткування нових форм співпраці з громадою
13	Сумська обласна державна телерадіокомпанія	повідомлення у випуску новин на радіо	12.12.08	провпровадження проекту в області
Публікації у електронних виданнях				
1	Сайт Тростянецької РР та РДА	www.trostanets-vlada.gov.ua Громади у реалізації проектів	26.11.08	Про проведення перших діалогів у громадах Тростянецького району
2	Сайт Тростянецької РР та РДА	Тростянецькі громади- учасники міжнародного проекту, www.trostanets-vlada.gov.ua	02.09.08	Інформація за результатами відбору сільських рад
3	Сайт Тростянецької РР та РДА	Пріоритет-водопостачання в Микитівці www.trostanets-vlada.gov.ua	04.09.08	Про семінар у Білківській сільській раді
4	Сайт Великописарівської РДА	http://www.vpisarivka-rda.narod.ru/invest_page_news.html	29.09.08	Про відбір сільських та селищних рад за конкурсом
5	Сайт Тростянецької РР та РДА	Тростянецькі громади- учасники міжнародного проекту, www.trostanets-vlada.gov.ua	02.09.08	Інформація за результатами відбору сільських рад
6	Сайт Тростянецької РР та РДА	Пріоритет-водопостачання в Микитівці www.trostanets-vlada.gov.ua	04.09.08	Про семінар у Білківській сільській раді
7	Сайт Великописарівської РДА	http://www.vpisarivka-rda.narod.ru/invest_page_news.html	29.09.08	Про відбір сільських та селищних рад за конкурсом

TERNOPILSKA OBALST

№	Назва видання	Назва публікації та посилання (для ел.ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	Вісті Придністров'я	Орієнтація на громаду.	26.09.08	Інформування про хід реалізації проекту в районі
6	Зборівська Дзвіниця	Проект МРГ ефективно реалізовується в Зборівському районі.	06.11.08	Розповідається про хід реалізації Проекту в Зборівському районі

7	Вісник Назбруччя	Чи справді громаду болить	19.12.08	Розповідається про участь громади смт.Гусятин в Проекті
8	Вільне Життя	Гнилиці та ООН партнери	19.12.08	Розповідається про хід реалізації Проекту в Тернопільській області
Телевізійні репортажі				
1	ТТБ (Телебачення)	Вісті ТТБ	17 .12.08	Розповідалося про підсумок роботи проекту МРГ в Тернопільській області та створення Координаційної ради
2	ТТБ (Телебачення)	Вісті ТТБ	18 .12.08	Розповідалося про підсумок роботи проекту МРГ в Тернопільській області та створення Координаційної ради
3	"Smile - TV" (Телебачення)	Телевізійні новини	17 .12.08	Розповідалося про підсумок роботи проекту МРГ в Тернопільській області та створення Координаційної ради
4	"Smile - TV" (Телебачення)	Телевізійні новини	18.12.08	Розповідалося про підсумок роботи проекту МРГ в Тернопільській області та створення Координаційної ради
Радіо репортажі				
1	Обласне радіо	Новини	17 грудня	Розповідалося коротко про підсумки Проекту в Тернопільській області та створення координаційної ради
2	Обласне радіо	Новини	18 грудня	Розповідалося коротко про підсумки Проекту в Тернопільській області та створення координаційної ради
3	Обласне радіо	Новини	18 грудня	Розповідалося коротко про підсумки Проекту в Тернопільській області та створення координаційної ради
Публікації у електронних виданнях (не рахуючи повідомлень на веб сайтах ОДА/ОР/РДА/РР/СВА)				
1	Smile - TV	Участь у проекті МРГ вже взяло 40 громад з Тернопільщини http://smiletv.te.ua/del/index.php?option=com_content&task=view&id=565&Itemid=1	17.12.08	Розповідається про результати діяльності та створення координаційної ради

VOLYNKA OBLAST

№	Назва видання	Назва публікації та посилання (для ел.ЗМІ)	Дата	Короткий зміст
Друковані публікації				
2	Іваничівська районна газета	Під лежачий камінь вода не тече	23.09.08	
Телевізійні репортажі				
3	Волинське обласне телебачення	репортаж в новинах	13.09 та 14.09	Про відібрані сільські ради та реалізацію проекту у Волинській області
4	Волинське обласне телебачення	репортаж в новинах	25.09 26.09	Про хід впровадження проекту у Волинській області
5	Волинське обласне телебачення	програма "Європейський простір"	жовтень 08	Про хід впровадження проекту у Волинській області
6	Волинське обласне телебачення	репортаж в новинах	16.12 та 17.12	хроніка координаційної ради, зокрема про впровадження проекту у Волинській області
Радіо репортажі				
3	Ковельська радіостанція	репортаж в новинах		Про хід проекту і участь в ньому Ковельського району

ZAPORIZKA OBLAST

№	Назва видання	Назва публікації та посилання (для ел.ЗМІ)	Дата	Короткий зміст
Друковані публікації				
17	"Голос Гуляйпільля"	"Проект МРГ- Перший діалог з громадою"	№77-01.10.08	Про проведення семінарів у сільських радах Гуляйпільського р-ну
18	"Запорізька правда"	"ООН поглиблює співробітництво із Запоріжжям"	№148-04.10.08	Про підписання угод між ООН, радами іа Адміністраціями

19	"Південна Зоря"	МРГ	№151-07.10.08	Про результати відбору сільських рад у Бердянському р-ні
20	"Пологівські вісті"	МРГ	№80-08.10.08	Про проведення семінарів у сільських радах у Пологівському районі
21	"Статус"-журнал	"На кону 4 милиона"	№41-13.10.08	Про підписання угод між ООН, радами та Адміністраціями
22	"Юг-інформ"	"Возьмите деньги, господа!"	№42-16.10.08	Про проведення семінару у Банівській с.радї та Приморському р-ні
23	"Приморская степь"	"Сами, сами...а мы поможем"	№41-18.10.08	Про проведення семінарів у сільських радах Приморського району
24	"Ринг-експрес"	"Есть ли манна небесная?"	№86-23.10.08	Про проведення семінарів у сільських радах Приморського району
25	"Рідний край"	"Перший діалог з громадою"	№87-25.10.08	Про проведення семінарів у сільських радах Куйбишевського району
26	"Нива"	"У районі реалізуються нові проекти"	№87-29.10.08	Про проведення семінарів у сільських радах Чернігівського району
27	"Время и мы"	" Не дожидаясь помощи "сверху", Великобелозерцы будут решать свои проблемы сообща"	№44-30.10.08	Про проведення семінарів у сільських радах Великобілозерського району
28	"Наше життя"	"Ніхто не виділяє гроші сонним людям"	№81-01.11.08	Про проведення семінарів у сільських радах Новомиколаївського району
29	"Південна Зоря"	МРГ	№169-06.11.08	Про проведення семінарів у сільських радах Бердянського району
30	"Наше життя"	"Перші кроки вселяють надію"	№83-08.11.08	Про створення ГО та обрання активу на загальних зборах у відібраних селах Новомиколаївського району
31	"Рідний край"	"Шанс для сільських громад"	№94-19.11.08	Про можливість створення ГО вирішити деякі нагальні місцеві проблеми та покращити інфраструктуру
32	"Ринг-експрес"	"Вам дрова не нужны?"	№96-27.11.08	Про проведення загальних зборів у с.Банівка та інших селах Приморського району
33	"Ринг-експрес"	"Караклия" начинает действовать"	№98-04.12.08	Про активність громади с.Гюнівка щодо участі у Проекті СВА

Радіо та телевізійні репортажі

6	ТВ "Алекс"	у області підписано Угоди з ОДА, ОР та районами	01.10.08	Про підписання угод між ООН, Радами та Адміністраціями
7	ТВ "Запорожье"	у області підписано Угоди з ОДА, ОР та районами	01.10.08	Про підписання угод між ООН, Радами та Адміністраціями
8	ТВ "Запорожье"	Інтерв'ю Губернатора Запорожской обл.	21.10.08	Про важливість впровадження Проекту СВА та покращення інфраструктури завдяки проекту
9	Обласне радіо-3	у області підписано Угоди з ОДА, ОР та районами	01.10.08	Про підписання угод між ООН, Радами та Адміністраціями
10	Радіо "Азовські хвилі"	В Бердянському районі пройшли загальні збори	27.11.08	Про проведення загальних зборів у відібраних селах Бердянського району

ZAKARPATSKA OBLAST

№	Назва видання	Назва публікації та посилання (для ел.ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	"Народне слово"	Форум місцевого розвитку.	20.12.08	Створений Форум місцевого розвитку сприятиме розвитку регіону, вирішенню проблем громад, стане доброю школою для представників місцевого самоврядування.
2	"Вісник Берегівщини"	Форум місцевого розвитку-ще один крок до розвитку...	18.12.08	Створений Форум місцевого розвитку сприятиме розвитку регіону, вирішенню проблем громад, стане доброю школою для представників місцевого самоврядування.
3	"Голос Верховини"	Форум місцевого розвитку (місцеве самоврядування дасть добрий результат)	13.12.08	Створений Форум місцевого розвитку сприятиме розвитку регіону, вирішенню проблем громад, стане доброю школою для представників місцевого самоврядування.
Телевізійні репортажі				
1	1+1	1-й діалог у громаді с.Боржава Проекту МРГ, коментар у новини	Лис.08	відеорепортаж про хід проведення діалогу в громаді, коментар щод здач проекту, ролі громад у місцевому розвитку

2	ТРК Тиса	репортаж у новини, провдення тренінгу напсання МПП у м.Міжгір'я	24.12.08	відзнято хід проведення тренінгу напсання МПП
Радіо репортажі				
1	"ТРК Тиса"	коментар у новини	24.10.08	етап реалізації Проекту МРГ в Закарпатській області
2	ТРК "М -Студіо"	коментар у новини	12.11.08	інформування слухачів про хід реалізації Проекту
Публікації у електронних виданнях (не рахуючи повідомлень на веб сайтах ОДА/ОП/РДА/РР/СВА)				
1	Ужгород нет уа	http://www.uzhgorod.net.ua/news/32632	20.11.08	20 листопада 08 р. в Закарпатській області було завершено проведення семінарів та перших діалогів з громадою в пілотних радах області.

ZHYTOMYRSKA OBLAST

№	Назва видання	Назва публікації та посилання (для ел.ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	газета "Нове життя"	"Перше завдання - допомагати людям"	07.11.08	інтерв'ю сільського голови про впровадження проекту
2	"Коростишівська газета"	Проект "Місцевий розвиток, орієнтований на громаду - в дії"	28.11.08	Про перший ФМР
3	"Новини Андрушівщини"			Про тренінги, які проходили в районі
4	газета "Вісті"	"Добробут власними руками"	28.11.08	про ФМР в Червоноармійському районі
5	газета "Новини Андрушівщини"	замітка без назви	17.10.08	про впровадження проекту в с. Любимівка
6	газета "Новини Андрушівщини"	"Активізація роботи громади"	03.10.08	Анонс інформації про Проект СВА
7	газета "Новини Андрушівщини"	"Відбувся тренінг-семінар"	24.10.08	Про проведення тренінгів для ГО
8	газета "Вісті"	"Соколівська громада дбає про своє майбутнє"	05.12.08	Про хід проекту СВА в Соколівській сільській раді
9	газета "Новини Андрушівщини"	МРГ	10.10.08	Про хід Проекту СВА в Андрушівському районі
Телевізійні репортажі				
1	Місцевий телеканал "Верховина"	Репортаж в новинах	15.11.08	Про ФМР в Коростишівському районі

Annex - 13.

List of Participants of Steering Committee Meeting

SN	Institution	Representative	Designation
1	Secretariat of the Cabinet of Ministers of Ukraine, Department for Regional Policy	Volodymyr Yatsiuk	Head of Department for Regional Policy
2	Ministry of Regional Development and Construction	Vyacheslav Negoda	Deputy Minister
3		Ms. Svitlana Sokolyk	Head of Department of European Integration, Department of International Cooperation, Investments and European Integration
4		Ms. Olga Shevchuk	Executive Officer of Department of European Integration, Department of International Cooperation, Investments and European Integration
5	Ministry of Communal Services	Oleksandr Savenko	Head of Department of Coordination of International Technical Assistance and External Relations
6	Ministry of Agricultural Policy	Vasyl Shapoval	Director of Department of Development of Rural Areas
7	Ministry of Economy	Yuriy Voloshyn	Head of Unit, Department of International Technoical Assistance
8	Ministry of Transport	Iryna Viter	Chief Specialist of Department and Coordination of Transport and Communication Systems
9	Foundation for local self-government under President of Ukraine	Oleksandr Beyko	Head of Unit of International Relations
10	Association of Cities and Communities of Ukraine	Oleksiy Moryev	Head of Department of Sustainable Development
11	Association of Village, Settlement and Town Councils of Ukraine	Poltavets Valentyna Dmytrivna	Deputy Head of Executive Director
12	EC Delegation Office to Ukraine	Laura Garagnani	Head of Operations
13		Myroslava Didukh	Sector Manager
14	United Nations Development Programme, Ukraine	Joanna Kazana-Wisniowiecka	Deputy Resident Representative
15		Oksana Remiga	Sr. Programme Manager
